



Document G702™ - 1992

Application and Certificate for Payment

TO OWNER: Madison County Board of Supervisors 125 West North Street Canton, MS 39046	PROJECT: Madison County Courtroom & Administration Area Renovations 146 W Center Street Canton, MS 39046	APPLICATION NO: 002	Distribution to:
FROM Flagstar Construction Company, Inc.	VIA JH&H Architects PA	PERIOD TO: October 31, 2017	OWNER:
CONTRACTOR: 2006 Aspen Cove Brandon, MS 39042	ARCHITECT: 1047 North Flowood Drive Flowood, MS 39232-9533	CONTRACT FOR: General Construction	ARCHITECT:
		CONTRACT DATE:	CONTRACTOR:
		PROJECT NOS: 17-100 / 1479 /	FIELD:
			OTHER:

CONTRACTOR'S APPLICATION FOR PAYMENT

Application is made for payment, as shown below, in connection with the Contract. Continuation Sheet, AIA Document G703, is attached.

- 1. ORIGINAL CONTRACT SUM \$ 416,500.00
- 2. NET CHANGE BY CHANGE ORDERS \$ 0.00
- 3. CONTRACT SUM TO DATE (Line 1 ± 2) \$ 416,500.00
- 4. TOTAL COMPLETED & STORED TO DATE (Column G on G703) \$ 65,749.50
- 5. RETAINAGE:
 - a. 5 % of Completed Work
(Column D + E on G703) \$ 3,287.48
 - b. 5 % of Stored Material
(Column F on G703) \$ 0.00
 - Total Retainage (Lines 5a + 5b or Total in Column I of G703) \$ 3,287.48
- 6. TOTAL EARNED LESS RETAINAGE \$ 62,462.03
(Line 4 Less Line 5 Total)
- 7. LESS PREVIOUS CERTIFICATES FOR PAYMENT \$ 17,299.03
(Line 6 from prior Certificate)
- 8. CURRENT PAYMENT DUE \$ 45,163.00
- 9. BALANCE TO FINISH, INCLUDING RETAINAGE
(Line 3 less Line 6) \$ 354,037.98

CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous months by Owner	\$ 0.00	\$ 0.00
Total approved this Month	\$ 0.00	\$ 0.00
TOTALS	\$ 0.00	\$ 0.00
NET CHANGES by Change Order	\$	0.00

The undersigned Contractor certifies that to the best of the Contractor's knowledge, information and belief the Work covered by this Application for Payment has been completed in accordance with the Contract Documents, that all amounts have been paid by the Contractor for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown herein is now due.

CONTRACTOR:
By: [Signature] Date: October 31, 2017

State of: Mississippi
County of: Rankin

Subscribed and sworn to before
me this 31st day of October 2017

Notary Public:
My Commission expires:



ARCHITECT'S CERTIFICATE FOR PAYMENT

In accordance with the Contract Documents, based on on-site observations and the data comprising this application, the Architect certifies to the Owner that to the best of the Architect's knowledge, information and belief the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

AMOUNT CERTIFIED \$ 45,163.00
(Attach explanation if amount certified differs from the amount applied. Initial all figures on this Application and on the Continuation Sheet that are changed to conform with the amount certified.)

ARCHITECT:
By: [Signature] Date: 11-6-2017

This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or Contractor under this Contract.

[Signature] 11/15/2017



AIA®

Document G703™ - 1992

Continuation Sheet

AIA Document, G702™-1992, Application and Certification for Payment, or G736™-2009, Project Application and Project Certificate for Payment, Construction Manager as Adviser Edition, containing Contractor's signed certification is attached.

In tabulations below, amounts are in US dollars.

Use Column I on Contracts where variable retainage for line items may apply.

APPLICATION NO: 002

APPLICATION DATE: 10/31/2017

PERIOD TO: 10/31/2017

ARCHITECT'S PROJECT NO: 17-100

A ITEM NO.	B DESCRIPTION OF WORK	C SCHEDULED VALUE	D WORK COMPLETED		F MATERIALS PRESENTLY STORED (NOT IN D OR E)	G TOTAL COMPLETED AND STORED TO DATE (D+E+F)		H BALANCE TO FINISH (C - G)	I RETAINAGE (IF VARIABLE RATE)
			FROM PREVIOUS APPLICATION (D + E)	THIS PERIOD		% (G ÷ C)			
	DIVISION 01	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
1	Bonds and Insurance	6,438.50	6,438.50	0.00	0.00	6,438.50	100.00 %	0.00	0.00
2	Sales Tax	14,577.50	637.00	1,664.00	0.00	2,301.00	15.78 %	12,276.50	0.00
3	ALLOWANCES:	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	1. Contingency	25,000.00	0.00	0.00	0.00	0.00	0.00 %	25,000.00	0.00
	2. Hardware	6,000.00	0.00	0.00	0.00	0.00	0.00 %	6,000.00	0.00
4	Mobilization	3,068.00	3,068.00	0.00	0.00	3,068.00	100.00 %	0.00	0.00
5	Project Coordinator	2,289.00	70.00	444.00	0.00	514.00	22.46 %	1,775.00	0.00
6	Project Supervision	38,050.00	1,142.00	7,382.00	0.00	8,524.00	22.40 %	29,526.00	0.00
7	Temporary Facilities	992.00	30.00	193.00	0.00	223.00	22.48 %	769.00	0.00
8	Dumpster	3,980.00	120.00	772.00	0.00	892.00	22.41 %	3,088.00	0.00
9	Temporary Construction	1,788.00	0.00	894.00	0.00	894.00	50.00 %	894.00	0.00
10	Final Cleaning	2,780.00	0.00	0.00	0.00	0.00	0.00 %	2,780.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 02	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
11	Demolition	19,859.00	3,972.00	5,958.00	0.00	9,930.00	50.00 %	9,929.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 03	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
12	Misc CMU/Angle Labor	1,318.00	0.00	0.00	0.00	0.00	0.00 %	1,318.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 05	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00

AIA Document G703™ - 1992. Copyright © 1963, 1965, 1966, 1967, 1970, 1978, 1983 and 1992 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 16:09:22 on 10/30/2017 under Order No.2125693182_1 which expires on 12/04/2017, and is not for resale.

User Notes:

(1851863634)

ITEM NO.	DESCRIPTION OF WORK	SCHEDULED VALUE	WORK COMPLETED		MATERIALS PRESENTLY STORED (NOT IN D OR E)	TOTAL COMPLETED AND STORED TO DATE (D+E+F)		BALANCE TO FINISH (C - G)	RETAINAGE (IF VARIABLE RATE)
			FROM PREVIOUS APPLICATION (D + E)	THIS PERIOD		% (G + C)			
13	Misc Steel Material	1,035.00	0.00	0.00	0.00	0.00	0.00 %	1,035.00	0.00
14	Steel Labor	2,730.00	0.00	0.00	0.00	0.00	0.00 %	2,730.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 06	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
15	Rough Carpentry	2,389.00	0.00	598.00	0.00	598.00	25.03 %	1,791.00	0.00
16	Rough Carpentry Labor	993.00	0.00	249.00	0.00	249.00	25.08 %	744.00	0.00
17	Wood Paneling and Millwork (Southeastern Architectural Woodwork):	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	1. Shop Drawings, Mobilization	5,104.00	0.00	1,276.00	0.00	1,276.00	25.00 %	3,828.00	0.00
	2. IT Workroom/A166	265.00	0.00	0.00	0.00	0.00	0.00 %	265.00	0.00
	3. Courtroom North/C104	6,261.00	0.00	0.00	0.00	0.00	0.00 %	6,261.00	0.00
	4. Courtroom East, South & West/C104	3,524.00	0.00	0.00	0.00	0.00	0.00 %	3,524.00	0.00
	5. Judge's Bench	37,802.00	0.00	0.00	0.00	0.00	0.00 %	37,802.00	0.00
	6. Gallery Wall	13,059.00	0.00	0.00	0.00	0.00	0.00 %	13,059.00	0.00
	7. Small Courtroom (Alt #3)	5,660.00	0.00	0.00	0.00	0.00	0.00 %	5,660.00	0.00
	8. Large Courtroom (Alt #3)	5,660.00	0.00	0.00	0.00	0.00	0.00 %	5,660.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 07	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
18	Thermal Insulation	1,239.00	0.00	310.00	0.00	310.00	25.02 %	929.00	0.00
19	Thermal Insulation Labor	874.00	0.00	219.00	0.00	219.00	25.06 %	655.00	0.00

AIA Document G703™ – 1992. Copyright © 1963, 1965, 1966, 1967, 1970, 1978, 1983 and 1992 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 16:09:22 on 10/30/2017 under Order No.2125693182_1 which expires on 12/04/2017, and is not for resale.

User Notes:

(1851863634)

A ITEM NO.	B DESCRIPTION OF WORK	C SCHEDULED VALUE	D WORK COMPLETED		F MATERIALS PRESENTLY STORED (NOT IN D OR E)	G TOTAL COMPLETED AND STORED TO DATE (D+E+F)		H BALANCE TO FINISH (C - G)	I RETAINAGE (IF VARIABLE RATE)
			FROM PREVIOUS APPLICATION (D + E)	THIS PERIOD		% (G + C)			
20	Blown Insulation	2,100.00	0.00	0.00	0.00	0.00	0.00 %	2,100.00	0.00
21	Joint Sealants	1,160.00	0.00	290.00	0.00	290.00	25.00 %	870.00	0.00
22	Joint Sealant Labor	662.00	0.00	166.00	0.00	166.00	25.08 %	496.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 08	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
23	Hollow Metal Frames	11,431.00	0.00	2,858.00	0.00	2,858.00	25.00 %	8,573.00	0.00
24	Metal Door Frame Labor	636.00	0.00	160.00	0.00	160.00	25.16 %	476.00	0.00
25	Doors	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
26	Door Hanging Labor	596.00	0.00	0.00	0.00	0.00	0.00 %	596.00	0.00
27	Hardware Labor	1,687.00	0.00	0.00	0.00	0.00	0.00 %	1,687.00	0.00
28	Glazing	3,135.00	0.00	0.00	0.00	0.00	0.00 %	3,135.00	0.00
29	Bullet Proof Glass	1,162.00	0.00	1,162.00	0.00	1,162.00	100.00 %	0.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 09	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
30	Gypsum Board Assemblies	5,210.00	0.00	782.00	0.00	782.00	15.01 %	4,428.00	0.00
31	Gypsum Board Labor	2,870.00	0.00	439.00	0.00	439.00	15.30 %	2,431.00	0.00
32	Metal Framing Material	4,233.00	0.00	635.00	0.00	635.00	15.00 %	3,598.00	0.00
33	Metal Framing Labor	8,163.00	0.00	1,225.00	0.00	1,225.00	15.01 %	6,938.00	0.00
34	Acoustical Ceilings	3,533.00	0.00	530.00	0.00	530.00	15.00 %	3,003.00	0.00
35	Acoustical Ceiling Labor	2,230.00	0.00	335.00	0.00	335.00	15.02 %	1,895.00	0.00
36	Finish Flooring (Byrd & Cook):	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	1. Resilient Material	3,131.00	0.00	0.00	0.00	0.00	0.00 %	3,131.00	0.00
	2. Resilient Labor	1,835.00	0.00	0.00	0.00	0.00	0.00 %	1,835.00	0.00
	3. Carpet Material	36,689.00	0.00	0.00	0.00	0.00	0.00 %	36,689.00	0.00

AIA Document G703™ – 1992. Copyright © 1963, 1965, 1966, 1967, 1970, 1978, 1983 and 1992 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 16:09:22 on 10/30/2017 under Order No.2125693182_1 which expires on 12/04/2017, and is not for resale.

User Notes:

(1851863634)

A ITEM NO.	B DESCRIPTION OF WORK	C SCHEDULED VALUE	D WORK COMPLETED		F MATERIALS PRESENTLY STORED (NOT IN D OR E)	G		H BALANCE TO FINISH (C - G)	I RETAINAGE (IF VARIABLE RATE)
			FROM PREVIOUS APPLICATION (D + E)	THIS PERIOD		TOTAL COMPLETED AND STORED TO DATE (D+E+F)	% (G + C)		
	4. Carpet Labor	6,118.00	0.00	0.00	0.00	0.00	0.00 %	6,118.00	0.00
37	Acoustical Floor Assemblies	954.00	0.00	0.00	0.00	0.00	0.00 %	954.00	0.00
38	Paint Materials	20,068.00	0.00	5,017.00	0.00	5,017.00	25.00 %	15,051.00	0.00
39	Paint Labor	8,601.00	0.00	2,150.00	0.00	2,150.00	25.00 %	6,451.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 10	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
40	Signage	3,434.00	0.00	0.00	0.00	0.00	0.00 %	3,434.00	0.00
41	Signage Labor	252.00	0.00	0.00	0.00	0.00	0.00 %	252.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 12	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
42	Courtroom Furnishings (Business Interiors):	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	1. 2ea-Lawyer Tables	8,809.00	0.00	0.00	0.00	0.00	0.00 %	8,809.00	0.00
	2. 1ea-Lectern	2,468.00	0.00	0.00	0.00	0.00	0.00 %	2,468.00	0.00
	3. 5ea-Armless Chairs	1,129.00	0.00	0.00	0.00	0.00	0.00 %	1,129.00	0.00
	4. 3ea-Mid-Back Chairs w/ Arms	1,087.00	0.00	0.00	0.00	0.00	0.00 %	1,087.00	0.00
43	Wooden Benches (Sauder Manufacturing):	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	1. Submittal Design	3,360.00	0.00	0.00	0.00	0.00	0.00 %	3,360.00	0.00
	2. Manufacturing Materials	6,336.00	0.00	0.00	0.00	0.00	0.00 %	6,336.00	0.00
	3. Installation	1,507.00	0.00	0.00	0.00	0.00	0.00 %	1,507.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 21	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
44	Existing Fire	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00


AIA Document G703™ – 1992. Copyright © 1963, 1965, 1966, 1967, 1970, 1978, 1983 and 1992 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 16:09:22 on 10/30/2017 under Order No.2125693182_1 which expires on 12/04/2017, and is not for resale.

User Notes:

(1851863634)

ITEM NO.	DESCRIPTION OF WORK	SCHEDULED VALUE	WORK COMPLETED		MATERIALS PRESENTLY STORED (NOT IN D OR E)	TOTAL COMPLETED AND STORED TO DATE (D+E+F)	% (G ÷ C)	BALANCE TO FINISH (C - G)	RETAINAGE (IF VARIABLE RATE)
			FROM PREVIOUS APPLICATION (D + E)	THIS PERIOD					
	Sprinkler Modification for New Ceilings (Hi-Tek):								
	1. Material	2,018.00	0.00	505.00	0.00	505.00	25.02 %	1,513.00	0.00
	2. Labor	2,573.00	0.00	644.00	0.00	644.00	25.03 %	1,929.00	0.00
	3. Engineering	525.00	0.00	525.00	0.00	525.00	100.00 %	0.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 23	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
45	Mechanical Sub (J.L. Roberts):	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	1. Mechanical Demo	1,575.00	500.00	550.00	0.00	1,050.00	66.67 %	525.00	0.00
	2. Ductwork Labor	1,575.00	0.00	735.00	0.00	735.00	46.67 %	840.00	0.00
	3. Ductwork Material	3,675.00	0.00	1,312.00	0.00	1,312.00	35.70 %	2,363.00	0.00
	4. Grilles Labor	1,050.00	0.00	525.00	0.00	525.00	50.00 %	525.00	0.00
	5. Grilles Material	1,417.00	0.00	630.00	0.00	630.00	44.46 %	787.00	0.00
	6. VAV	761.00	0.00	761.00	0.00	761.00	100.00 %	0.00	0.00
	7. HW Piping Labor	840.00	0.00	0.00	0.00	0.00	0.00 %	840.00	0.00
	8. HW Piping Material	368.00	0.00	0.00	0.00	0.00	0.00 %	368.00	0.00
	9. Insulation	2,888.00	0.00	0.00	0.00	0.00	0.00 %	2,888.00	0.00
	10. Controls	1,470.00	0.00	0.00	0.00	0.00	0.00 %	1,470.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	DIVISION 26	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
46	Electrical Sub (Bomac Electric):	0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	1. Mobilization	1,575.00	1,182.00	393.00	0.00	1,575.00	100.00 %	0.00	0.00
	2. Electrical Demo	2,625.00	1,050.00	0.00	0.00	1,050.00	40.00 %	1,575.00	0.00
	3. Pipe/Wire Rough In	4,766.00	0.00	1,910.00	0.00	1,910.00	40.08 %	2,856.00	0.00

ITEM NO.	DESCRIPTION OF WORK	SCHEDULED VALUE	WORK COMPLETED		MATERIALS PRESENTLY STORED (NOT IN D OR E)	TOTAL COMPLETED AND STORED TO DATE (D+E+F)		BALANCE TO FINISH (C - G)	RETAINAGE (IF VARIABLE RATE)
			FROM PREVIOUS APPLICATION (D + E)	THIS PERIOD		%	(G ÷ C)		
	4. Labor	7,140.00	0.00	2,856.00	0.00	2,856.00	40.00 %	4,284.00	0.00
	5. Lights	8,925.00	0.00	0.00	0.00	0.00	0.00 %	8,925.00	0.00
	6. Labor	1,470.00	0.00	0.00	0.00	0.00	0.00 %	1,470.00	0.00
	7. Trim Out	683.00	0.00	171.00	0.00	171.00	25.04 %	512.00	0.00
	8. Labor	1,260.00	0.00	315.00	0.00	315.00	25.00 %	945.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
		0.00	0.00	0.00	0.00	0.00	0.00 %	0.00	0.00
	GRAND TOTAL	\$416,500.00	\$18,209.50	\$47,540.00	\$0.00	\$65,749.50	15.79 %	\$350,750.50	\$0.00

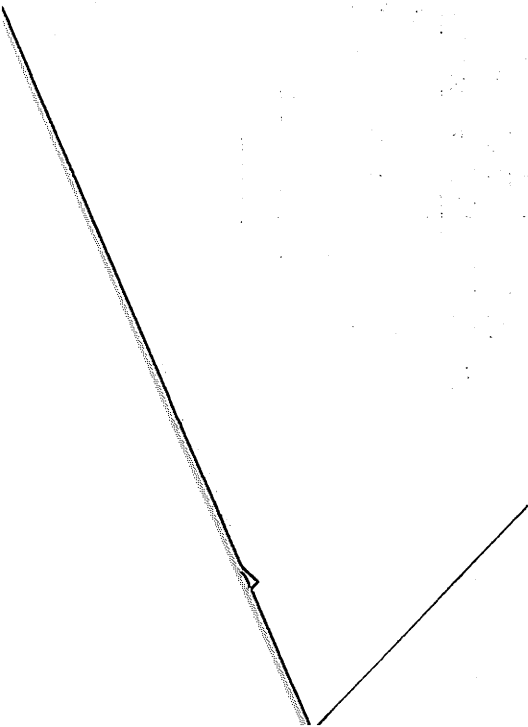


ID	Task Name	Duration	Start	Finish	Predecessors	2017		Qtr 4, 2017				Qtr 1, 2018		
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	
1	Madison County Courthouse	153 days	Tue 9/5/17	Tue 2/13/18										
2	Pre-Construction Activities	79 days	Tue 9/5/17	Wed 11/22/17										
3	Executed Contract	1 day	Tue 9/5/17	Tue 9/5/17										
4	Pre-Construction Meeting	1 day	Wed 9/13/17	Wed 9/13/17	3FS+7 days									
5	Submittals	45 days	Thu 9/14/17	Sat 10/28/17	4									
6	Procurement	63 days	Thu 9/21/17	Wed 11/22/17	5SS+7 days									
7	Notice to Proceed	1 day	Mon 9/25/17	Mon 9/25/17										
8	Construction Activities	133 days	Mon 9/25/17	Tue 2/13/18	7SS									
9	Mobilization	1 day	Mon 9/25/17	Mon 9/25/17										
10	Administration Area - North & South	92 days	Mon 9/25/17	Wed 1/3/18	7SS									
11	Build Temporary Wall @ Corridor - North	1 day	Mon 9/25/17	Mon 9/25/17										
12	Demo Wall, Ceilings, Flooring - North	6 days	Tue 9/26/17	Sun 10/1/17	11									
13	Demo MEPF - North	5 days	Wed 9/27/17	Sun 10/1/17	12SS+1 day									
14	Install Metal Wall Studs - North	3 days	Mon 10/2/17	Wed 10/4/17	13									
15	Install Wall MEPF Rough-In - North	4 days	Tue 10/3/17	Fri 10/6/17	14FS-2 days									
16	MEP In Wall Inspection - North	1 day	Mon 10/9/17	Mon 10/9/17	15FS+2 days									
17	Install MEP Above Ceiling Rough-In - North	13 days	Thu 10/5/17	Tue 10/17/17	15SS+2 days									
18	Install Wall Gyp. Board - North	7 days	Thu 10/5/17	Wed 10/11/17	14									
19	Install Wall Insulation - North	6 days	Thu 10/5/17	Tue 10/10/17	18SS									
20	Install HM Frames - North	2 days	Wed 10/11/17	Thu 10/12/17	19									
21	Tape/Float Gyp Walls - North	10 days	Fri 10/6/17	Sun 10/15/17	18SS+1 day,20									
22	Repair Gyp. Ceiling - North	2 days	Mon 10/9/17	Tue 10/10/17	21									
23	Install Subfloor Prep - North	1 day	Mon 10/16/17	Mon 10/16/17	22FS+5 days									
24	Install Flooring - North	2 days	Tue 10/17/17	Wed 10/18/17	23									
25	Install Primer & 1st Coat Paint - North	2 days	Thu 10/19/17	Fri 10/20/17	24									
26	Install Ceiling Grid - North	2 days	Sat 10/21/17	Sun 10/22/17	25									
27	Complete MEPF Drops - North	2 days	Mon 10/23/17	Tue 10/24/17	26									
28	Install Accoustic Sealants - North	1 day	Wed 10/25/17	Wed 10/25/17	27									
29	Above Ceiling MEP Inspection - North	1 day	Wed 10/25/17	Wed 10/25/17	27									
30	Install Ceiling Tile - North	1 day	Thu 10/26/17	Thu 10/26/17	29									
31	MEPF Testing - North	1 day	Fri 10/27/17	Fri 10/27/17	30									
32	Install Metal Furdown Studs - North	1 day	Sat 10/28/17	Sat 10/28/17	31									
33	Install Gyp/Tape/Float/ Prime Furdown - North	2 days	Sun 10/29/17	Mon 10/30/17	32									

Project: Madison County Courthouse Date: Thu 10/12/17	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	2017		Qtr 4, 2017			Qtr 1, 2018		
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
34	Install HM Storefront - North	2 days	Tue 10/31/17	Wed 11/1/17	33								
35	Install WD Droos - North	2 days	Thu 11/2/17	Fri 11/3/17	34								
36	Install Glazing - North	1 day	Sat 11/4/17	Sat 11/4/17	35								
37	Install Door Hardware - North	2 days	Sat 11/4/17	Sun 11/5/17	36SS								
38	Install Millwork - North	1 day	Mon 11/13/17	Mon 11/13/17	37								
39	Install Final Coat of Paint - North	2 days	Tue 11/14/17	Wed 11/15/17	38								
40	Install Rubber Base - North	2 days	Thu 11/16/17	Fri 11/17/17	39								
41	Complete MEP Devices/Trim - North	2 days	Thu 11/16/17	Fri 11/17/17	40SS								
42	Final Clean - North	1 day	Sat 11/18/17	Sat 11/18/17	41								
43	Owner Punchlist Walk Thru- North	3 days	Sun 11/19/17	Tue 11/21/17	42								
44	Owner Move In - North	1 day	Wed 11/22/17	Wed 11/22/17	43								
45	Build Temporary Wall @ Corridor - South	1 day	Mon 11/27/17	Mon 11/27/17	44								
46	Demo Wall, Ceilings, Flooring - South	2 days	Tue 11/28/17	Wed 11/29/17	45								
47	Demo MEPF - South	2 days	Wed 11/29/17	Thu 11/30/17	46SS+1 day								
48	Install Metal Wall Studs - South	2 days	Fri 12/1/17	Sat 12/2/17	47								
49	Install Wall MEP Rough-In - South	1 day	Sun 12/3/17	Sun 12/3/17	48								
50	MEP In Wall Inspection - South	1 day	Mon 12/4/17	Mon 12/4/17	49								
51	Install MEP Above Ceiling Rough-In - South	2 days	Mon 12/4/17	Tue 12/5/17	50SS								
52	Install Wall Gyp. Board - South	3 days	Wed 12/6/17	Fri 12/8/17	51								
53	Install Wall Insulation - South	2 days	Wed 12/6/17	Thu 12/7/17	52SS								
54	Tape/Float Gyp Walls - South	2 days	Sat 12/9/17	Sun 12/10/17	52								
55	Install Primer & 1st Coat Paint - South	2 days	Mon 12/11/17	Tue 12/12/17	54								
56	Install Ceiling Grid	1 day	Wed 12/13/17	Wed 12/13/17	55								
57	Above Ceiling MEP Inspection - South	1 day	Thu 12/14/17	Thu 12/14/17	56								
58	Complete MEP Drops	1 day	Fri 12/15/17	Fri 12/15/17	57								
59	Install Ceiling Tile	1 day	Sat 12/16/17	Sat 12/16/17	58								
60	MEPF Testing - South	1 day	Sun 12/17/17	Sun 12/17/17	59								
61	Install Subfloor Prep - South	1 day	Mon 12/18/17	Mon 12/18/17	60								
62	Install HM Frames - South	1 day	Tue 12/19/17	Tue 12/19/17	61								
63	Install Flooring - South	2 days	Wed 12/20/17	Thu 12/21/17	62								
64	Install Rubber Base - South	1 day	Fri 12/22/17	Fri 12/22/17	63								
65	Install WD Droos - South	1 day	Wed 12/27/17	Wed 12/27/17	64								
66	Install Glazing - South	1 day	Thu 12/28/17	Thu 12/28/17	65								


Project: Madison County Courthouse Date: Thu 10/12/17	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	2017		Qtr 4, 2017			Qtr 1, 2018		
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
67	Install Door Hardware - South	1 day	Thu 12/28/17	Thu 12/28/17	65								
68	Install Final Coat of Paint - South	2 days	Fri 12/22/17	Wed 12/27/17	63								
69	Complete MEP Devices/Trim - South	1 day	Thu 12/28/17	Thu 12/28/17	68								
70	Final Clean - South	1 day	Fri 12/29/17	Fri 12/29/17	69								
71	Owner Punchlist Walk Thru- South	3 days	Sat 12/30/17	Tue 1/2/18	70								
72	Owner Move-In - South	1 day	Wed 1/3/18	Wed 1/3/18	71								
73	New Courtroom	74 days	Mon 11/27/17	Tue 2/13/18	44								
74	Demo Walls, Ceiling, Flooring	10 days	Mon 11/27/17	Wed 12/6/17	44								
75	Demo MEPF	9 days	Tue 11/28/17	Wed 12/6/17	74SS+1 day								
76	Install Fiberglass Over Window	1 day	Thu 12/7/17	Thu 12/7/17	75								
77	Install MEPF Above Ceiling Rough-In	10 days	Thu 12/7/17	Sat 12/16/17	76SS								
78	Install Metal Stud Walls/Furr Down	4 days	Sun 12/10/17	Wed 12/13/17	77SS+3 days								
79	Install Furdown	3 days	Thu 12/14/17	Sat 12/16/17	78								
80	Install MEP In-Wall Rough-In	4 days	Thu 12/14/17	Sun 12/17/17	78								
81	In-Wall MEP Inspection	1 day	Mon 12/18/17	Mon 12/18/17	80								
82	Cut Slab for Floor Boxes	1 day	Tue 12/19/17	Tue 12/19/17	81								
83	Install Electrical Floor Rough-In	2 days	Wed 12/20/17	Thu 12/21/17	82								
84	Install Wall Insulation	2 days	Fri 12/22/17	Wed 12/27/17	83								
85	Install Gyp. Board Walls	2 days	Thu 12/28/17	Fri 12/29/17	84								
86	Install Gyp. Board Ceilings	2 days	Sat 12/30/17	Sun 12/31/17	85								
87	Tape, Float, Finish Gyp Board	3 days	Tue 1/2/18	Thu 1/4/18	86								
88	Install Door Frames	1 day	Fri 1/5/18	Fri 1/5/18	87								
89	Install Primer & 1st Coat Paint	2 days	Sat 1/6/18	Sun 1/7/18	88								
90	Install Ceiling Grid	3 days	Mon 1/8/18	Wed 1/10/18	89								
91	Complete MEPF Drops	4 days	Thu 1/11/18	Sun 1/14/18	90								
92	Above Ceiling MEP Inspection	1 day	Mon 1/15/18	Mon 1/15/18	91								
93	Install Metal Bracing for Millwork	2 days	Mon 1/15/18	Tue 1/16/18	92SS								
94	Built Platform for Judges Bench	3 days	Wed 1/17/18	Fri 1/19/18	93								
95	Install Floor Prep	1 day	Sat 1/20/18	Sat 1/20/18	94								
96	Install Carpet/VCT/Base	3 days	Sun 1/21/18	Tue 1/23/18	95								
97	Install Doors	2 days	Wed 1/24/18	Thu 1/25/18	96								
98	Install Millwork	5 days	Wed 1/24/18	Sun 1/28/18	97SS								
99	Install Final Paint	3 days	Mon 1/29/18	Wed 1/31/18	98								



Project: Madison County Courthouse Date: Thu 10/12/17	Task		Milestone		External Task	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	2017		Qtr 4, 2017			Qtr 1, 2018		
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
100	Install Hardware	2 days	Thu 2/1/18	Fri 2/2/18	99								
101	Install Glass	1 day	Sat 2/3/18	Sat 2/3/18	100								
102	Install MEP Trim Devices	3 days	Sun 2/4/18	Tue 2/6/18	101								
103	Install Specialties	2 days	Sun 2/4/18	Mon 2/5/18	102SS								
104	Install Furniture	1 day	Tue 2/6/18	Tue 2/6/18	103								
105	Install Benches	1 day	Wed 2/7/18	Wed 2/7/18	104								
106	Final Clean	2 days	Thu 2/8/18	Fri 2/9/18	105								
107	Owner Punchlist Walk Thru	3 days	Sat 2/10/18	Mon 2/12/18	106								
108	Owner Move-In	1 day	Tue 2/13/18	Tue 2/13/18	107								
109	Small Courtroom	11 days	Mon 11/13/17	Mon 11/27/17									
110	Demo Carpet	2 days	Mon 11/13/17	Tue 11/14/17									
111	Install Millwork	1 day	Wed 11/15/17	Wed 11/15/17	110								
112	Install Carpet	1 day	Thu 11/16/17	Thu 11/16/17	111								
113	Stain Millwork	1 day	Fri 11/17/17	Fri 11/17/17	112								
114	Paint Walls	2 days	Fri 11/17/17	Sat 11/18/17	113SS								
115	Final Clean	1 day	Sun 11/19/17	Sun 11/19/17	114								
116	Owner Punchlist Walk Thru	3 days	Mon 11/20/17	Wed 11/22/17	115								
117	Owner Move-In	1 day	Mon 11/27/17	Mon 11/27/17	116								
118	Large Courtroom	11 days	Tue 11/28/17	Fri 12/8/17									
119	Demo Carpet	2 days	Tue 11/28/17	Wed 11/29/17	117								
120	Install Millwork	1 day	Thu 11/30/17	Thu 11/30/17	119								
121	Install Carpet	1 day	Fri 12/1/17	Fri 12/1/17	120								
122	Stain Millwork	1 day	Sat 12/2/17	Sat 12/2/17	121								
123	Paint Walls	2 days	Sat 12/2/17	Sun 12/3/17	122SS								
124	Final Clean	1 day	Mon 12/4/17	Mon 12/4/17	123								
125	Owner Punchlist Walk Thru	3 days	Tue 12/5/17	Thu 12/7/17	124								
126	Owner Move-In	1 day	Fri 12/8/17	Fri 12/8/17	125								



Project: Madison County Courthouse Date: Thu 10/12/17	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
