

## **YANDELL ROAD EAST SEGMENT MADISON COUNTY BOARD OF SUPERVISORS 1<sup>ST</sup> QUARTER 2025 UPDATE**

Begin Contract Time: November 4, 2024

Contract Value: \$1,291,578.50

Amount Billed (3/31/25): \$182,937.72

Project Schedule: See Attached

Work Completed During Reporting Period:

- Topographic Mapping and Utility Survey
- Initial Resource Agency Consultation Completed
- T & E Consultation with USFWS Completed (Bat Surveys)
- Cultural Resource Survey complete and reports submitted to MDAH for concurrence



Work Planned for Next Reporting Period:

- Wetland Delineation and Submit to USACE for Concurrence
- Complete Noise Study
- Complete ROW Survey
- Conduct Geotechnical Investigations
- Continue Working on Field Review Plans (60% Plans)

Conceptual Design Approach:

Yandell Road will be symmetrically widened to a 4-lane undivided section from the BOP to the EOP. ROW will be purchased to accommodate a 5-lane section along the entire length of the project. This will allow, as this section of Yandell Road is developed, for 5-lane sections to be constructed at all future subdivision entrances.

# **EXHIBIT C** **ESTIMATED PROJECT SCHEDULE** **YANDELL ROAD EAST SEGMENT** **BAINBRIDGE CROSSING TO SR 43**

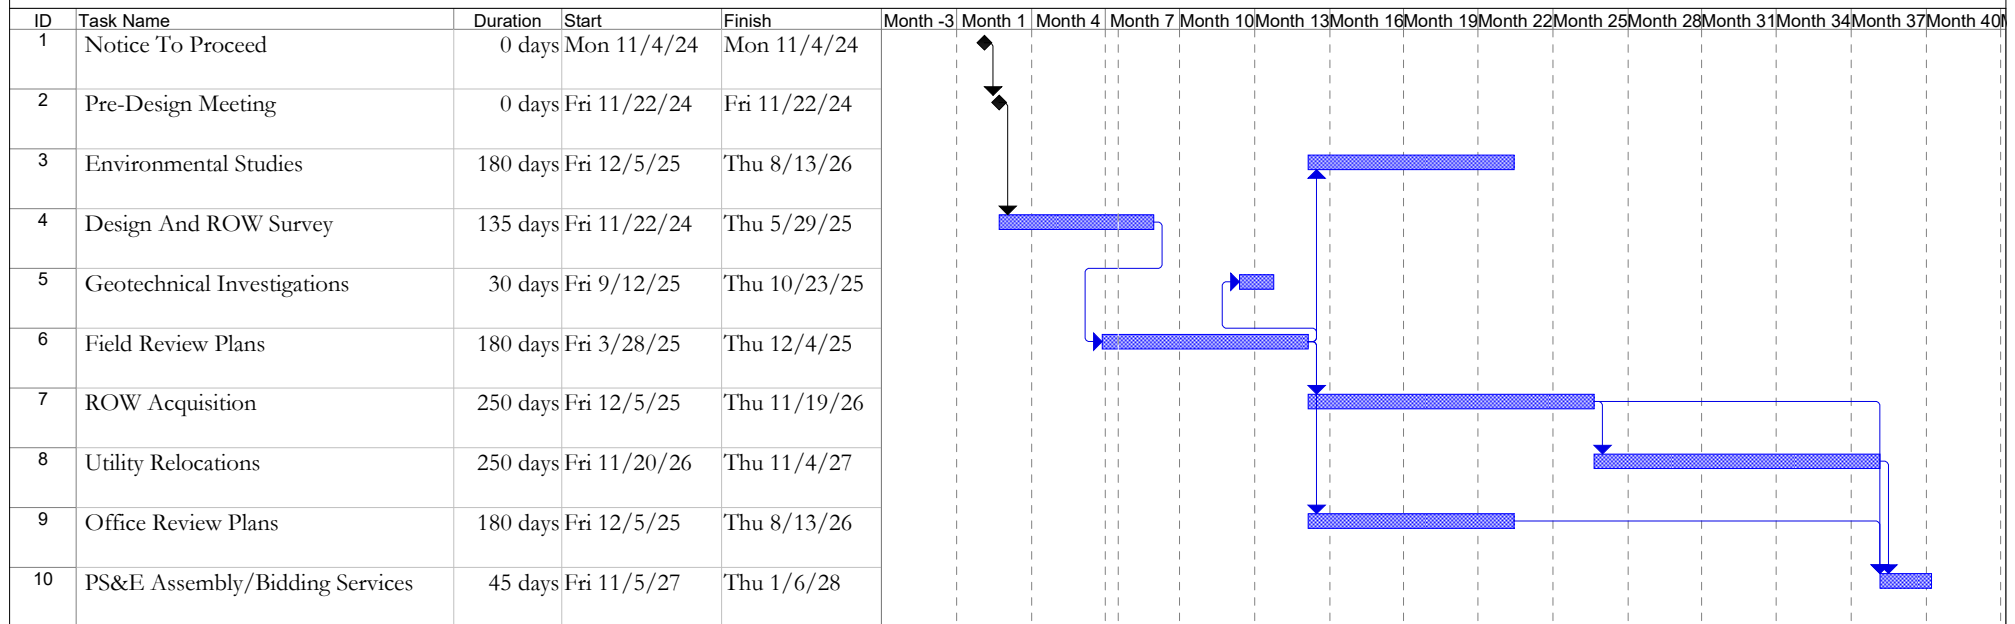

|  |                 |  |                    |  |                       |  |                    |  |
|--|-----------------|--|--------------------|--|-----------------------|--|--------------------|--|
|  | Task            |  | External Tasks     |  | Duration-only         |  | External Tasks     |  |
|  | Split           |  | External MileTask  |  | Manual Summary Rollup |  | External Milestone |  |
|  | Milestone       |  | Inactive Milestone |  | Manual Summary        |  | Progress           |  |
|  | Summary         |  | Inactive Summary   |  | Start-only            |  | Split              |  |
|  | Project Summary |  | Manual Task        |  | Finish-only           |  |                    |  |
