

## Yandell Rd. Intersection Improvements at North Old Canton Rd. STP-7024-00(001)LPA 109649/701000 Project Status Update

July 21<sup>st</sup>, 2025


- Date Contract began: November 18<sup>th</sup>, 2024.
- Value of Contract:
  - Original: **\$357,676.04**
  - o SA #1: \$64,695.15
  - Current Total: **\$422,371.19**
- Amount Billed (as of 07/15/2025): \$128,872.47 (30%)
- Project Schedule: See Attached
- Work completed:
  - Survey work is complete
  - Bridge and Roadway Geotechnical Reports are complete.
  - Bridge Hydraulics are Complete
  - $\circ$   $\,$  LPA 100 has been approved by MDOT  $\,$
  - LPA 700 has been approved by MDOT
  - o Environmental Studies are underway (Phase 1 Cultural,
  - Field Review Plans 90% Complete
  - Bridge Plans 90% Complete
- Work planned for upcoming quarter:
  - **o** Finish Environmental Studies and Obtain Environmental Approval
  - Have Field Review Meeting
  - Begin Right Of Way Acquisition
  - Finalize Bridge Widening and Replacement Plans

						U	PDATE	D PRO	JECT	SCHEE	DULE								
	YAN	IDELL	RD. SI	GNAL					OLD					AL IMP	ROVE	MENTS	)		
					MA				OARD										
		2	024	1		STP	-7024-	00(001	)LPA 1	<b>09649/</b> 025	701000					T			
Task Description	Duration	Nov.	Dec.	Jan.	Feb.	Mar.	Apr.	May	June	July	Aug.	Sept.	Oct.	Nov.	Dec.	Jan.	Feb.	Mar.	A
	Months																		
Contract Negotiation & Execution	1		COMPLETE														UPDAT	ED: 07	/17/
			COMPLETE																
Topographic & Boundary Survey	1				COMPLETE												Notes:		
					COMPLETE												1. This s firms on		
Preliminary Engineering (Exhibits, Layouts, & LPA Docs)	3																	after ini	
	3					COMPLETE											2. All act month u		
																	3. Right	of Way,	Envi
Phase A, Bridge Widening Plans	6						$\square$			COMPLETE							and time	elines ar	e sul
Environmental Studies & Permitting (Bridge & Roadway)	8						$\searrow$										T. AND NOV.		
														EXPECTED	APPROVALE		T. AND NOV.		
Right of Way Acquisition (For Bridge Widening)	5																		
Phase A, Prelim. Design (Roadway & Traffic Signal Plans)	9																		_
																EXPECTED	COMPLETION	IN LATE AU	GUST
Right of Way Acquisition (For Roadway & Signal)	8																		
Utility Relocation & Coordination (Bridge & Roadway)	15																		
Phase B, Final Design and Final Plans (Bridge Widening)	3													EXDECTED	COMPLETIO				
														EXPECTED		IN IN SEPT.			
Final Plan Review (Bridge Widening)	1																		
Bidding & Contractor Award (Bridge Widening)	2																		
Phase B, Design Design (Roadway & Traffic Signal Plans)	6																		
Final Plan Review (Roadway & Signal)	2																		
Bidding & Contractor Award (Roadway & Signal)	2																		
																			-

Brandon | 601.591.1077 Flowood | 601.627.7780 Madison | 769.289.0031 Est. 2004

	20	26				
Apr.	May	June	July	Aug.	Sept.	Oct.
7/25						
1/25						
ill be di	irectly im	inacted b	ov engine	ering		
	e intersec					
	dination.					
deadiii erwise r	nes reflec	ct the las	t date of	the		
	nental &	Utility Re	elocation	dates		
subject	to chang	ge.				
IST						



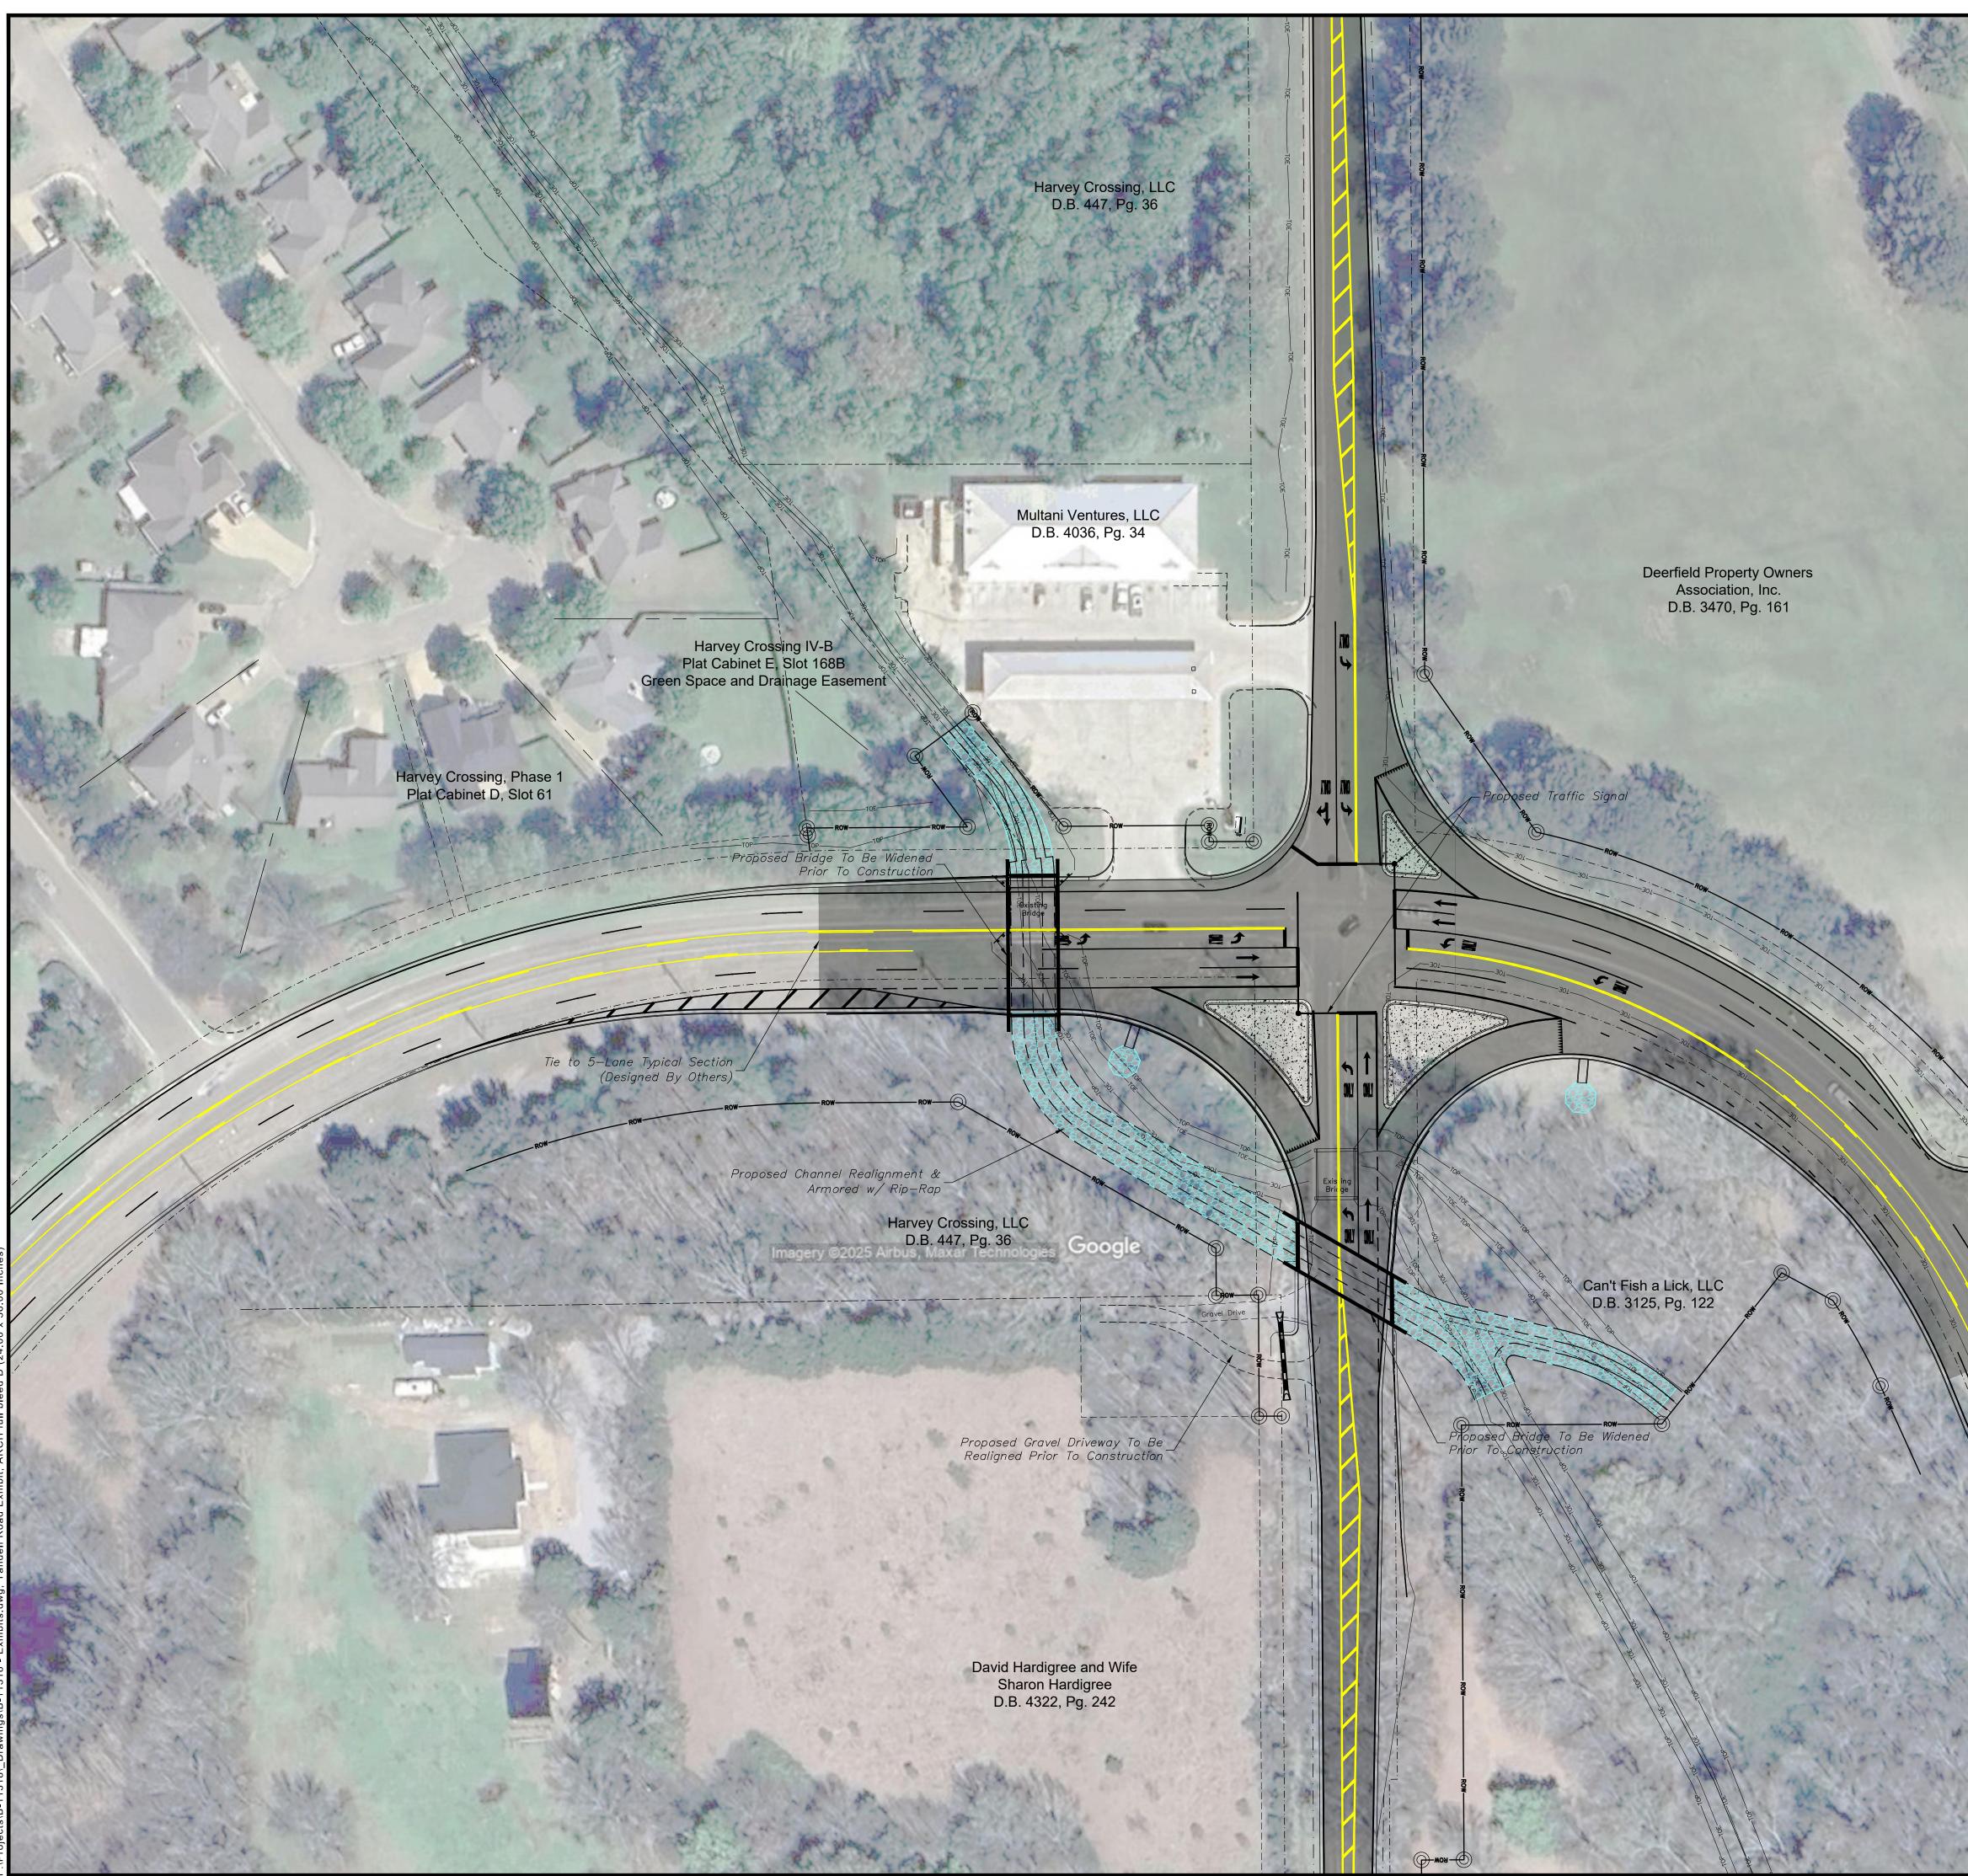

NOT FOR CONSTRUCTION	BENGINEERING & SURVEYING, LLC ENGINEERING & SURVEYING, LLC CIVIL • STRUCTURAL • PLANNING • SURVEYING • UAV MAPPING BRANDON   FLOWOOD   MADISON EST. 2004 www.benchmarkms.net 601-627-7780
	TON AT N. OLDDATE: 07/14/25DRAM1: JBHREVISIONS:CHECKED: OLBSCALE: 1"=50'Revisions:Revisions:REF C/L:REF C/L:EG SURFACE:EG SURFACE:EG SURFACE:N, MS 39046FG SURFACE:FG SURFACE:EG SURFACE:
	PROJECT LOCATION: YANDELL RD INTERSECTIO CANTON, RMS 39046 CLIENT: MADISON COUNTY BOARD 125 W. NORTH ST CANTON, J
The to 5-Lane Typical Section Clesigned By Others:	PROJECT: PROJECT: STP-7024-00(001)LPA/109649-701000 I SHEET CONTENTS: YANDELL ROAD EXHIBIT PLUTAD EXHIBIT
