


**Yandell Rd. Intersection Improvements at North Old Canton Rd.
STP-7024-00(001)LPA 109649/701000**

Project Status Update

October 20th, 2025

- Date Contract began: **November 18th, 2024.**
- Value of Contract:
 - Original: **\$357,676.04**
 - SA #1: **\$64,695.15 (Bridge & Hydraulic Design)**
 - SA#2: **\$149,013.10 (ROW Acquisition)**
 - Current Total: **\$571,384.29**
- Amount Billed (*as of 10/10/25*): **\$180,961.70 (32% of total)**
- Updated Project Schedule: **See Attached**
- Work completed:
 - **Survey work is complete**
 - **Bridge and Roadway Geotechnical Field Work Reports are complete.**
 - **Bridge Hydraulics are Complete**
 - **LPA 100 has been approved by MDOT**
 - **LPA 700 has been approved by MDOT**
 - **Environmental:**
 - **(Phase 1 Cultural Is completed and has been submitted to MDOT)**
 - **Wetlands and Other Waters report is complete**
 - **MDOT has determined a public meeting will not be necessary.**
 - **Field Inspection Plans were submitted to MDOT on September 8th, 2025.**
 - **Field Inspection Meeting was held on October 7th, 2025**
 - **Bridge Plans 90% Complete, waiting on Env. Permits, ROW Acquisition and Utility Relocation**
 - **Final ROW Plans are Complete, Preparing to begin ROW Phase when ENV is approved**
- Work planned for upcoming quarter:
 - **Design and Office Review Plan Production**
 - **Complete Environmental work and obtain Environmental Approval**
 - **Have ROW Kick Off Meeting and Begin Right of Way Acquisition**
 - **Finalize Bridge Widening and Replacement Plans & Specifications**

MADISON COUNTY BOARD OF SUPERVISORS
YANDELL ROAD SIGNAL INSTALLATION AT NORTH OLD CANTON RD.

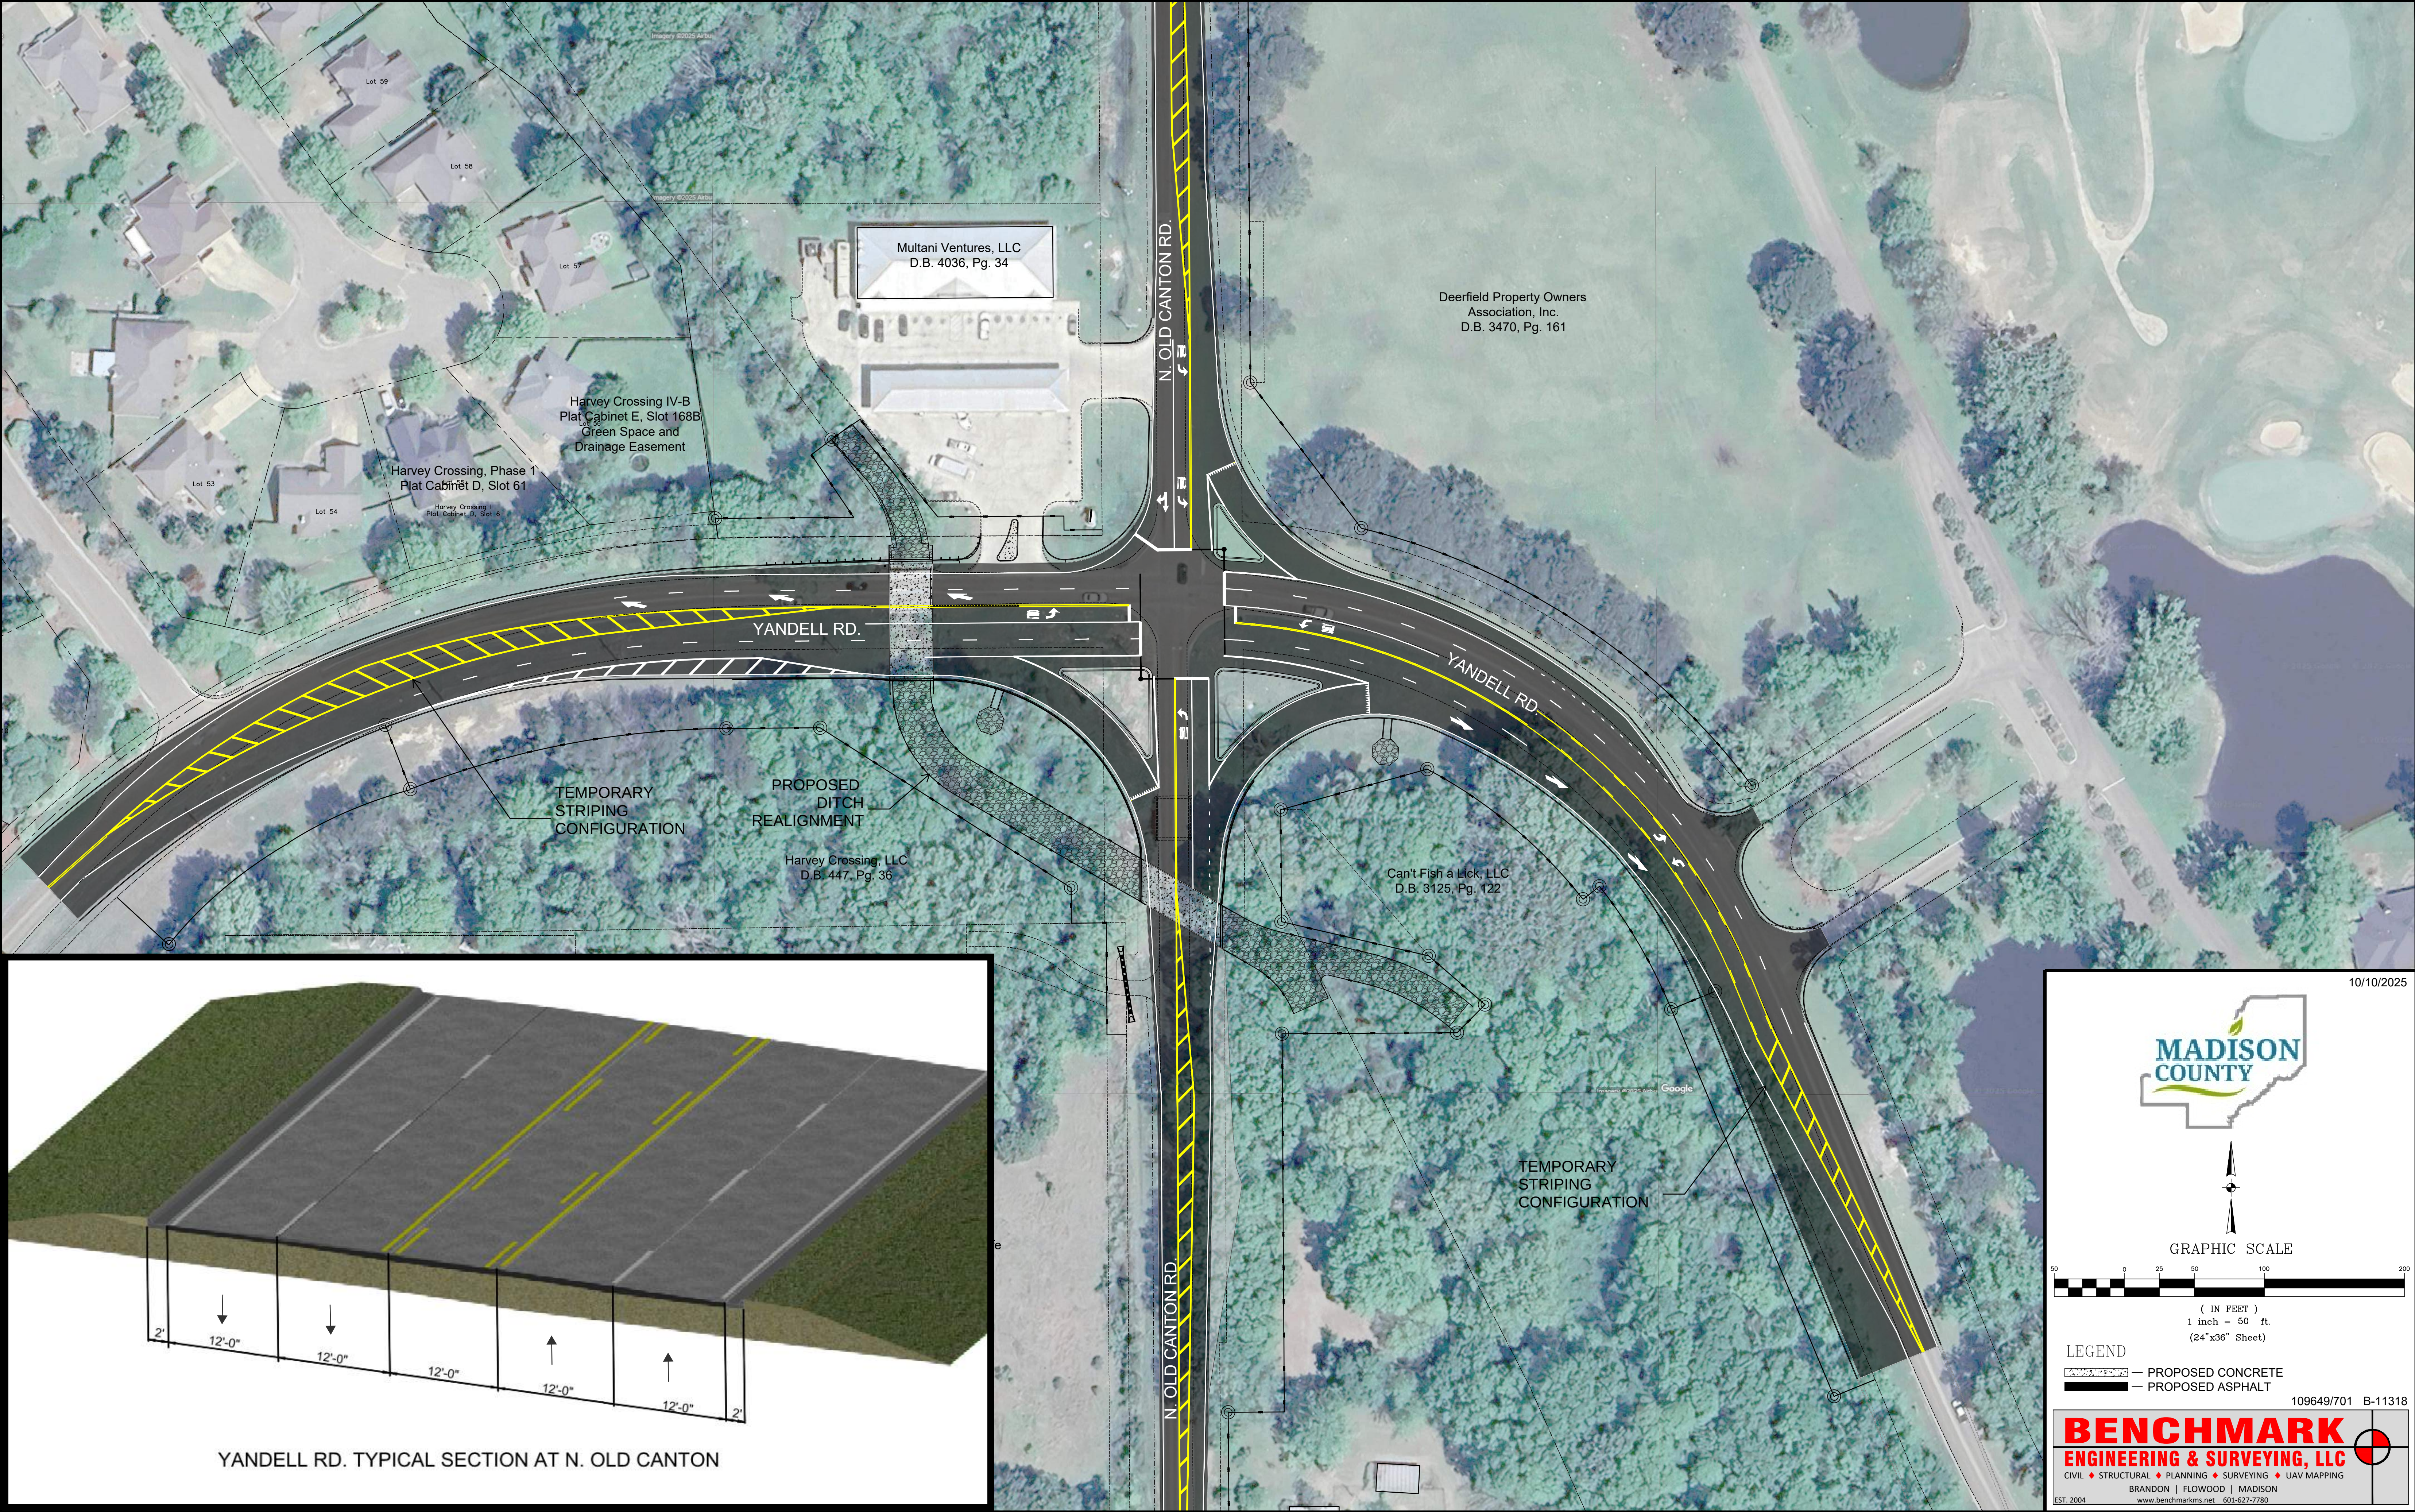

UPDATED PROJECT SCHEDULE																												
YANDELL RD. SIGNAL INSTALLATION AT NORTH OLD CANTON (AND ADDITIONAL IMPROVEMENTS)																												
MADISON COUNTY BOARD OF SUPERVISORS																												
STP-7024-00(001)LPA 109649/701000																												
Task Description	Duration	2024		2025												2026												
		Nov.	Dec.	Jan.	Feb.	Mar.	Apr.	May	June	July	Aug.	Sept.	Oct.	Nov.	Dec.	Jan.	Feb.	Mar.	Apr.	May	June	July	Aug.	Sept.	Oct.			
	Months																											
Contract Negotiation & Execution	1		COMPLETE														UPDATED: 10/10/25											
																	Notes: 1. This schedule will be directly impacted by engineering firms on both sides of the intersection and any design changes after initial coordination. 2. All actual dates/deadlines reflect the last date of the month unless otherwise noted. 3. Right of Way, Environmental & Utility Relocation dates and timelines are subject to change. 4. Red represents a projected or actual delay depending on where it's shown.											
Topographic & Boundary Survey	1				COMPLETE																							
Preliminary Engineering (Exhibits, Layouts, & LPA Docs)	3					COMPLETE																						
Phase A, Bridge Widening Plans	6									COMPLETE								EXPECTED APPROVAL IN DECEMBER										
Environmental Studies & Permitting (Bridge & Roadway)	9																											
Right of Way Acquisition (For Bridge Widening)	8																											
Phase A, Prelim. Design (Roadway & Traffic Signal Plans)	10															COMPLETE												
Right of Way Acquisition (For Roadway & Signal)	6																											
Utility Relocation & Coordination (Bridge & Roadway)	14																											
Phase B, Final Design and Final Plans (Bridge Widening)	3														90% COMPLETE, WAITING ON ENV, ROW, & UTILITY													
Final Plan Review (Bridge Widening)	1																											
Bidding & Contractor Award (Bridge Widening)	2																											
Phase B, Design Design (Roadway & Traffic Signal Plans)	6																											
Final Plan Review (Roadway & Signal)	2																											
Bidding & Contractor Award (Roadway & Signal)	2																											
