

August 16, 2017

Mr. Danny Lee
Madison County - Buildings and Grounds
PO Box 608
Canton, Mississippi 39046-0608

Re: Madison County Courthouse - Cupola Repairs & Restoration
Canton, Mississippi
Application for Payment # 2
BSA Project #1208.3

Mr. Lee:

Please find enclosed Three (3) Paramount Construction Group, LLC's **Application for Payment # 2** for work completed during the period of July 18, 2017 to August 15, 2017. We have reviewed work included while on-site August 15, 2017, discussed adjustments with the Contractor and all submitted information and take no exception to submitted adjusted amount requested. We therefore recommend payment to Paramount Construction Group, LLC for the amount of **\$96,586.28**.

Three (3) Days were requested due to inclement weather as part of this Application for Payment. See Attached Letter as prepared by Paramount Construction Group, LLC, Dated August 16, 2017.

Please contact us if you have questions.

Sincerely,

Craig E. Bjorgum, AIA
Belinda Stewart Architects, P.A.

Cc: Paramount Construction Group, LLC (E-mail)
BSA Job File

APPLICATION AND CERTIFICATION FOR PAYMENT

TO OWNER: Madison County Board of Supervisors PROJECT: Courthouse Cupola Repairs & Restoration APPLICATION NO: 2 Distribution to:

ADDRESS: 125 W North Street OWNER

FROM GENERAL CONTRACTOR: Paramount Construction Group, LLC ADDRESS: Canton, MS 39046 PERIOD FROM: 7/18/2017 ARCHITECT

234 West School Street, Suite B PERIOD TO: 8/15/2017 CONTRACTOR

Ridgeland, MS 39157 ARCH. PROJECT NO: 1208.3

FROM SUBCONTRACTOR: _____ CONTR. PROJECT NO: 17125

CONTRACT FOR: Cupola Repairs & Restora COST CODE: _____ CONTRACT DATE: 05/15/17 DATE SUBMITTED: 08/15/17

CONTRACTOR'S APPLICATION FOR PAYMENT

Application is made for payment, as shown below, in connection with the Contract. Continuation Sheet, AIA Document G703, is attached.

1. ORIGINAL CONTRACT SUM	\$	327,967.00
2. Net change by Change Orders	\$	-
3. CONTRACT SUM TO DATE (Line 1 + 2)	\$	327,967.00
4. TOTAL COMPLETED & STORED TO DATE (Column G on G703)	\$	131,186.80
5. RETAINAGE:		
a. <u>5%</u> of Completed Work	\$	6,559.34
(Column D + E on G703)		
b. <u>0%</u> of Stored Material	\$	-
(Column F on G703)		
Total Retainage (Lines 5a + 5b or Total in Column I of G703)	\$	6,559.34
6. TOTAL EARNED LESS RETAINAGE (Line 4 Less Line 5 Total)	\$	124,627.46
7. LESS PREVIOUS CERTIFICATES FOR PAYMENT (Line 6 from prior Certificate)	\$	28,041.18
8. CURRENT PAYMENT DUE	\$	96,586.28
9. BALANCE TO FINISH, INCLUDING RETAINAGE (Line 3 less Line 6)	\$	203,339.54

CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous months	\$0.00	\$0.00
Total approved this Month	\$0.00	\$0.00
TOTALS	\$0.00	\$0.00
NET CHANGES by Change Order		\$0.00

The undersigned Contractor certifies that to the best of the Contractor's knowledge, information and belief the Work covered by this Application for Payment has been completed in accordance with the Contract Documents, that all amounts have been paid by the Contractor for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown herein is now due.

CONTRACTOR: Paramount Construction Group, LLC

By: [Signature] Date: 8/16/17

State of: Mississippi County of: Madison
 Subscribed and sworn to before me this 16th day of August
Eileen M. Hesterwood
June 1 2020

CERTIFICATE FOR PAYMENT

In accordance with the Contract Documents, based on on-site observations and the data comprising the application, the ~~Construction Manager~~ Architect certifies to the Owner that to the best of their knowledge, information and belief the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

AMOUNT CERTIFIED \$ 96,586.28 CB

(Attach explanation if amount certified differs from the amount applied. Initial all figures on this Application and on the Continuation Sheet that are changed to conform with the amount certified.)

~~CONSTRUCTION MANAGER~~ Architect
 By: [Signature] Date: _____
 ARCHITECT (IF APPLICABLE):
 By: [Signature] Date: 8/16/17

This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or Contractor under this Contract.

@ [Signature] Aug 16, 2017

CONTINUATION SHEET

APPLICATION AND CERTIFICATION FOR PAYMENT, containing Contractor's signed certification is attached.
 In tabulations below, amounts are stated to the nearest dollar.
 Use Column I on Contracts where variable retainage for line items may apply.

APPLICATION NO: 2.00
 APPLICATION DATE: 08/15/17
 PERIOD TO: 08/15/17
 ARCHITECT'S PROJECT NO:

A ITEM NO.	B DESCRIPTION OF WORK	C SCHEDULED VALUE	D WORK COMPLETED		F MATERIALS PRESENTLY STORED (NOT IN D OR E)	G TOTAL COMPLETED AND STORED TO DATE (D+E+F)		H BALANCE TO FINISH (C - G)	I RETAINAGE (IF VARIABLE RATE)
			FROM PREVIOUS APPLICATION (D + E)	THIS PERIOD		% (G + C)			
1	Mobilization	\$ 16,398.35	\$ 16,398.35		\$ -	\$ 16,398.35	100.00%	\$ -	\$ 819.92
2	Scaffold & Fencing	\$ 65,593.40	\$ 13,118.68	\$ 39,356.04		\$ 52,474.72	80.00%	\$ 13,118.68	\$ 2,623.74
3	Lantern (Top of Cupola) Including Windows/Copper Etc.	\$ 49,195.05		\$ 46,735.30		\$ 46,735.30	95.00%	\$ 2,459.75	\$ 2,336.76
4	Main Dome (Copper)	\$ 16,398.35		\$ 15,578.43		\$ 15,578.43	95.00%	\$ 819.92	\$ 778.92
5	Interior Structural RPRS LVL/Brackets/Framing	\$ 36,076.37				\$ -	0.00%	\$ 36,076.37	\$ -
6	Cornise & Upper Section-Verticle siding & Paint	\$ 36,076.37				\$ -	0.00%	\$ 36,076.37	\$ -
7	Outriggers/Siding/Windows/Pilasters/Flashing/Paint								
	Side 1	\$ 6,764.33				\$ -	0.00%	\$ 6,764.33	\$ -
	Side 2	\$ 6,764.33				\$ -	0.00%	\$ 6,764.33	\$ -
	Side 3	\$ 6,764.33				\$ -	0.00%	\$ 6,764.33	\$ -
	Side 4	\$ 6,764.33				\$ -	0.00%	\$ 6,764.33	\$ -
	Side 5	\$ 6,764.33				\$ -	0.00%	\$ 6,764.33	\$ -
	Side 6	\$ 6,764.33				\$ -	0.00%	\$ 6,764.33	\$ -
	Side 7	\$ 6,764.30				\$ -	0.00%	\$ 6,764.30	\$ -
	Side 8	\$ 6,764.30				\$ -	0.00%	\$ 6,764.30	\$ -
8	Copper Skirt								
	Materials	\$ 18,038.19				\$ -	0.00%	\$ 18,038.19	\$ -
	Labor	\$ 18,038.19				\$ -	0.00%	\$ 18,038.19	\$ -
9	Lower Section Trim/Verticle Siding/Access Door/Paint	\$ 18,038.19				\$ -	0.00%	\$ 18,038.19	\$ -
PAGE TOTALS		\$327,967.00	\$29,517.03	\$101,669.77	\$0.00	\$131,186.80	40.00%	\$196,780.20	\$6,559.34

Contractor's Affidavit of Release of Liens

OWNER: Madison County Board of Supervisors
 ARCHITECT: Belinda Stewart Architects, PA
 CONTRACTOR: Paramount Construction Group,
 SURETY: _____
 OTHER: NONE

THIS DOCUMENT HAS IMPORTANT LEGAL CONSEQUENCES; CONSULTATION WITH AN ATTORNEY IS ENCOURAGED WITH RESPECT TO ITS COMPLETION OR MODIFICATION. AUTHENTICATION OF THIS ELECTRONICALLY DRAFTED AIA DOCUMENT MAY BE MADE BY USING AIA DOCUMENT D401.

TO OWNER: Madison County Board of Supervisors
 (Name and address)
 c/o 125 W North Street
 Canton, MS 39046

ARCHITECT'S PROJECT NO.: 1208.3

CONTRACT FOR: Cupola Repairs

PROJECT: Courthouse Cupola Repairs & Restoration
 (Name and address)
 125 W North Street
 Canton, MS 39046

CONTRACT DATED: 5/15/2017

The undersigned hereby certifies that to the best of the undersigned's knowledge, information and belief, except as listed below, the Releases or Waivers of Lien attached hereto include the Contractor, all Subcontractors, all suppliers of materials and equipment, and all performers of Work, labor or services who have or may have liens or encumbrances or the right to assert liens or encumbrances against any property of the Owner arising in any manner out of the performance of the contract referenced above:

EXCEPTIONS:
 NONE

CONTRACTOR:
 Paramount Construction Group, LLC
 234 West School Street, Suite B
 Ridgeland, MS 39157

SUPPORTING DOCUMENTS ATTACHED HERETO:

1. Contractor's Release or Waiver of Liens, conditional upon receipt of final payment.
2. Separate Releases or Waivers of liens from secondary Subcontractors and material and equipment suppliers, to the extend required by the Owner, accompanied by a list thereof if requested.

By: [Signature]
 (Signature of authorized representative)
Clint Bledsoe Project Manager
 (Printed name and title)



County of: Madison State of: Mississippi
 Subscribed and sworn to before me this 16 day of August
 Notary Public: Ellen M Hazlewood
 My Commission expires: June 1, 2020

AIA DOCUMENT G706A - CONTRACTOR'S AFFIDAVIT OF RELEASE OF LIENS - 1994 EDITION - AIA - COPYRIGHT 1994 - THE AMERICAN INSTITUTE OF ARCHITECTS, 1735 NEW YORK AVENUE N.W., WASHINGTON DC 20006-5292.. WARNING; Unlicensed photocopying violates U.S. copyright laws and is subject to legal prosecution. This document was electronically produced with permission of the AIA and can be reproduced without violation until the date of expiration as noted below.



PARAMOUNT
CONSTRUCTION
GROUP, LLC

234 West School Street, Suite B • Ridgeland, MS 39157 • 601-427-5454 office • 601-427-5456 fax

August 16, 2017

Craig E. Bjorgum, AIA
Belinda Stewart Architects, PA
61 North Dunn St.
Eupora, Mississippi 39744

Project: Madison County Courthouse – Cupola Repairs & Restoration

Subject: PCG Pay App #002 (Period to 8/15/17) – Inclement Weather Letter

Dear Mr. Bjorgum,

Per specification section 01 200 Price and Payment Procedures, paragraph 1.04 Applications for Progress Payments, this letter is to serve as the official request for inclement weather days. Please see below number of days requested for this pay period.

- As you will see in the attached daily reports and weather reports, the above referenced project experienced three (3) days of inclement weather the week of 8/6/17.

PCG will continue to work diligently to meet the overall project schedule, however, we do reserve our rights to claim these inclement weather days, should they be needed at the end of the project.

Should you have any questions and/or comments, please feel free to contact me.

Sincerely,

A handwritten signature in blue ink, appearing to read 'Clint Bledsoe', is written over a light blue circular stamp.

Clint Bledsoe
Project Manager

**HISTORIC RENOVATIONS OF YAZOO
333 NORTH MAIN STREET
YAZOO CITY, MS 39194**

JOB REPORT: 08/04, 2017

MADISON COUNTY COURTHOUSE CUPOLA
CANTON, MS

WEATHER Hot - Clear

ACTIONS Lantern - dome repairs
mock-up for non-sbg sistant pull test
wash test
met with Mark (structural engineer) to
show mock-up of lower LVL
discussed upper curved beam (new plan)
- will mock-up and resubmit

COMMENTS

**HISTORIC RENOVATIONS OF YAZOO
333 NORTH MAIN STREET
YAZOO CITY, MS 39194**

JOB REPORT: 08/07 2017

MADISON COUNTY COURTHOUSE CUPOLA
CANTON, MS

WEATHER Cloudy - scattered rain

ACTIONS Carpet prep + cleaning; sealing

COMMENTS

Weather History for KJAN - August, 2017

August

7

2017

View

Monday, August 7, 2017

Daily Weekly Monthly Custom


	Actual	Average	Record
Temperature			
Mean Temperature	81 °F	82 °F	
Max Temperature	89 °F	92 °F	102 °F (1947)
Min Temperature	73 °F	72 °F	62 °F (1900)
Degree Days			
Heating Degree Days	0	0	
Month to date heating degree days	0	0	
Since 1 June heating degree days	0	0	
Since 1 July heating degree days	0	0	
Cooling Degree Days	16	17	
Month to date cooling degree days	111	119	
Year to date cooling degree days	1542	1414	
Since 1 June cooling degree days	1046	1056	
Growing Degree Days	31 (Base 50)		

	Actual	Average	Record
Moisture			
Dew Point	75 °F		
Average Humidity	84		
Maximum Humidity	100		
Minimum Humidity	68		
Precipitation			
Precipitation	1.43 in	0.15 in	1.96 in (1983)
Month to date precipitation	1.94	1.09	
Year to date precipitation	49.11	34.13	
Sea Level Pressure			
Sea Level Pressure	29.98 in		
Wind			
Wind Speed	7 mph (South)		
Max Wind Speed	25 mph		
Max Gust Speed	34 mph		
Visibility	8 miles		
Events	Fog , Rain , Thunderstorm		

T = Trace of Precipitation, MM = Missing Value

Source: NWS Daily Summary

Daily Weather History Graph

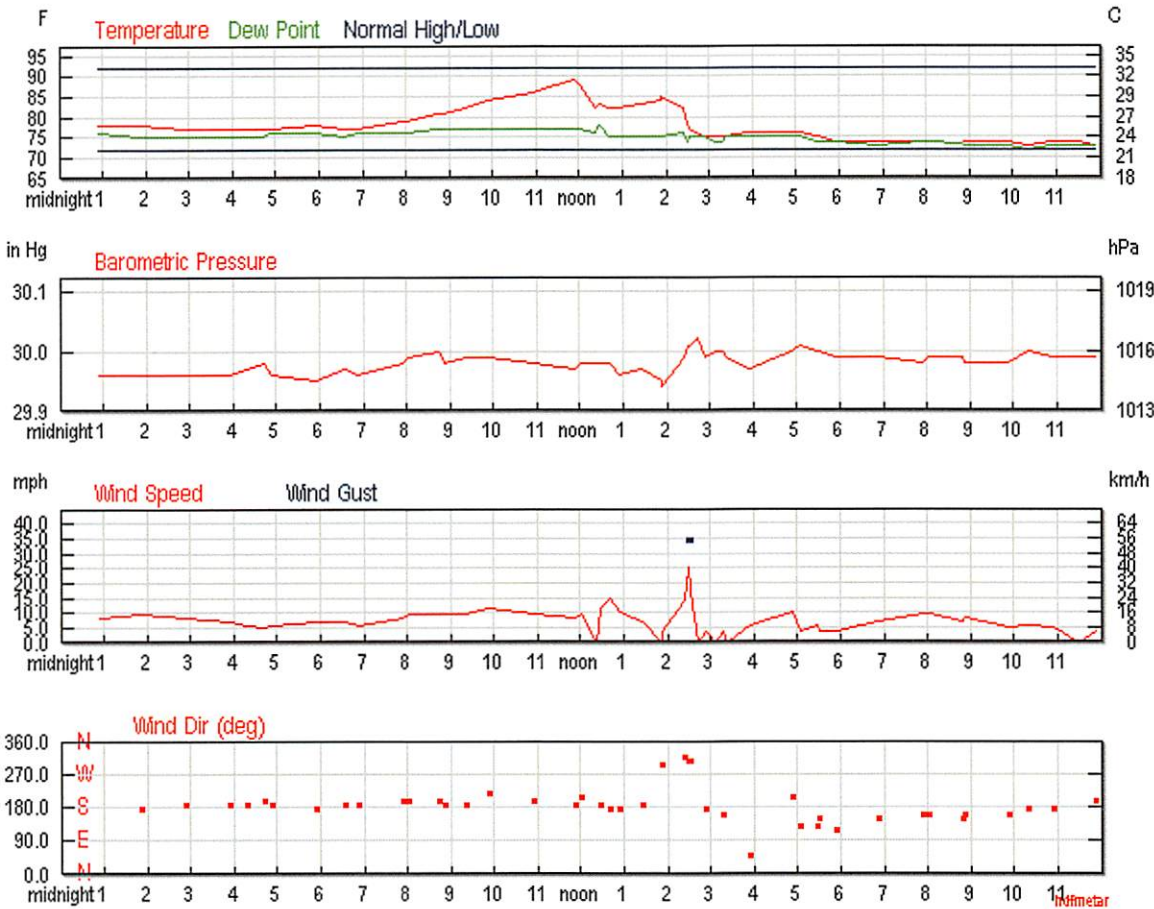

Search for Another Location

Airport or City:

Submit

Trip Planner

Search our weather history database for the weather conditions in past years. The results will help you decide how hot, cold, wet, or windy it might be!

Date:

Submit

Astronomy

Aug. 07, 2017

Rise

Set

Actual Time

6:19 AM CDT

7:52 PM CDT

**HISTORIC RENOVATIONS OF YAZOO
333 NORTH MAIN STREET
YAZOO CITY, MS 39194**

JOB REPORT: 06/08, 2017

MADISON COUNTY COURTHOUSE CUPOLA
CANTON, MS

WEATHER Rain

ACTIONS Lantern prep. and setting

COMMENTS

Weather History for KJAN - August, 2017

August

8

2017

View

Tuesday, August 8, 2017

Daily Weekly Monthly Custom


	Actual	Average	Record
Temperature			
Mean Temperature	76 °F	82 °F	
Max Temperature	79 °F	92 °F	104 °F (1935)
Min Temperature	73 °F	72 °F	58 °F (1989)
Degree Days			
Heating Degree Days	0	0	
Month to date heating degree days	0	0	
Since 1 June heating degree days	0	0	
Since 1 July heating degree days	0	0	
Cooling Degree Days	11	17	
Month to date cooling degree days	122	136	
Year to date cooling degree days	1553	1431	
Since 1 June cooling degree days	1057	1073	
Growing Degree Days	26 (Base 50)		

	Actual	Average	Record
Moisture			
Dew Point	74 °F		
Average Humidity	93		
Maximum Humidity	100		
Minimum Humidity	85		
Precipitation			
Precipitation	1.01 in	0.16 in	2.74 in (1948)
Month to date precipitation	2.95	1.25	
Year to date precipitation	50.12	34.29	
Sea Level Pressure			
Sea Level Pressure	30.01 in		
Wind			
Wind Speed	3 mph (East)		
Max Wind Speed	7 mph		
Max Gust Speed	9 mph		
Visibility	8 miles		
Events	Rain		

T = Trace of Precipitation, MM = Missing Value

Source: NWS Daily Summary

Daily Weather History Graph

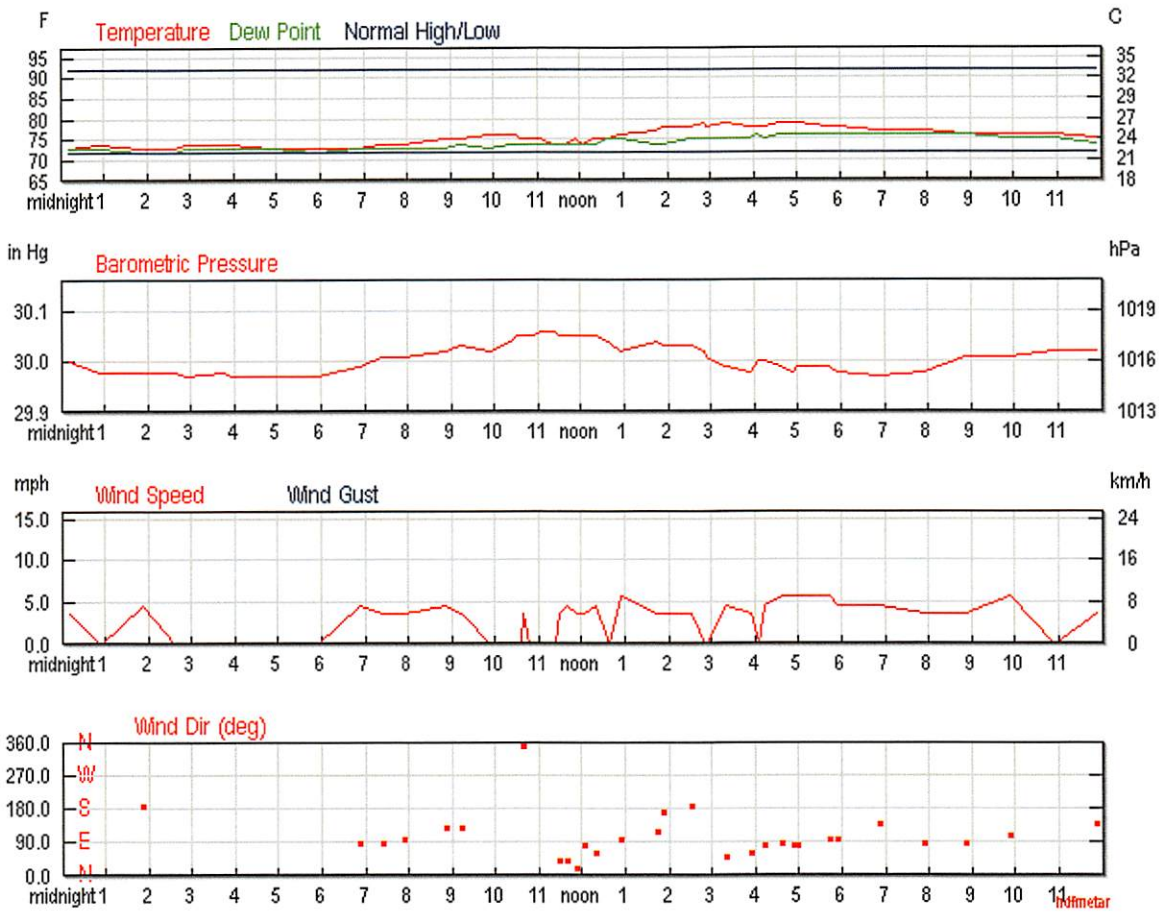

Search for Another Location

Airport or City:

Submit

Trip Planner

Search our weather history database for the weather conditions in past years. The results will help you decide how hot, cold, wet, or windy it might be!

Date:

Submit

Astronomy

Aug. 08, 2017

Rise

Set

Actual Time

6:19 AM CDT

7:51 PM CDT

**HISTORIC RENOVATIONS OF YAZOO
333 NORTH MAIN STREET
YAZOO CITY, MS 39194**

JOB REPORT: 07/09, 2017

MADISON COUNTY COURTHOUSE CUPOLA
CANTON, MS

WEATHER Rain

ACTIONS ————

COMMENTS

Jackson, MS

Jackson-Evers International

© 9:37 AM CDT on August 16, 2017 (GMT -0500)

Weather History for KJAN - August, 2017

August

9

2017

View

Wednesday, August 9, 2017


Daily	Weekly	Monthly	Custom		Actual	Average	Record
Temperature							
Mean Temperature					80 °F	82 °F	
Max Temperature					85 °F	92 °F	105 °F (1935)
Min Temperature					74 °F	71 °F	55 °F (1989)
Degree Days							
Heating Degree Days					0	0	
Month to date heating degree days					0	0	
Since 1 June heating degree days					0	0	
Since 1 July heating degree days					0	0	
Cooling Degree Days					15	17	
Month to date cooling degree days					137	153	
Year to date cooling degree days					1568	1448	
Since 1 June cooling degree days					1072	1090	
Growing Degree Days					28 (Base 50)		

	Actual	Average	Record
Moisture			
Dew Point	75 °F		
Average Humidity	90		
Maximum Humidity	100		
Minimum Humidity	80		
Precipitation			
Precipitation	0.43 in	0.16 in	3.99 in (1942)
Month to date precipitation	3.38	1.41	
Year to date precipitation	50.55	34.45	
Sea Level Pressure			
Sea Level Pressure	30.05 in		
Wind			
Wind Speed	3 mph (ESE)		
Max Wind Speed	18 mph		
Max Gust Speed	22 mph		
Visibility	8 miles		
Events	Rain , Thunderstorm		

T = Trace of Precipitation, MM = Missing Value

Source: NWS Daily Summary

Daily Weather History Graph

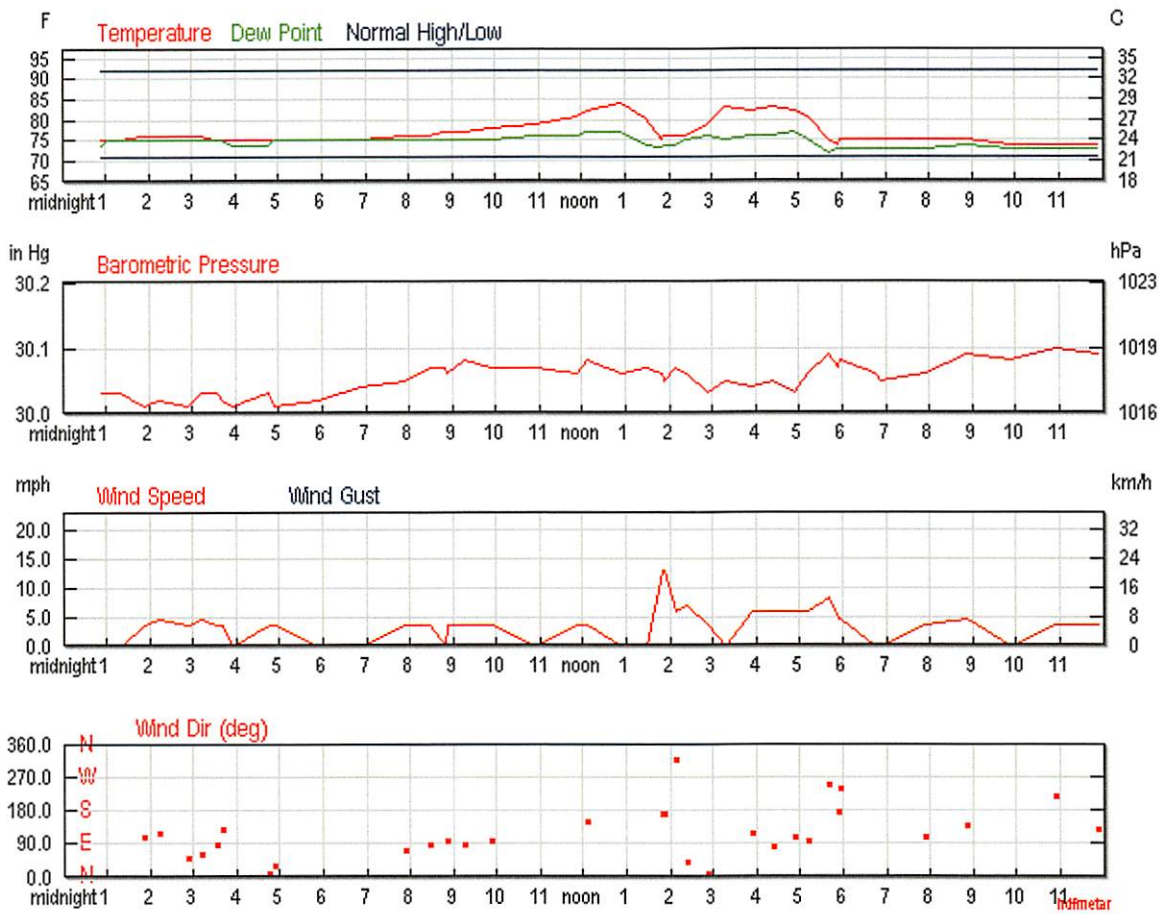

Search for Another Location

Airport or City:

Submit

Trip Planner

Search our weather history database for the weather conditions in past years. The results will help you decide how hot, cold, wet, or windy it might be!

Date:

Submit

Astronomy

Aug. 09, 2017

Rise

Set

Actual Time

6:20 AM CDT

7:50 PM CDT

Weather History for KJAN - August, 2017

August

10

2017

View

Thursday, August 10, 2017

Daily Weekly Monthly Custom


	Actual	Average	Record
Temperature			
Mean Temperature	78 °F	82 °F	
Max Temperature	84 °F	92 °F	103 °F (2007)
Min Temperature	72 °F	71 °F	59 °F (1989)
Degree Days			
Heating Degree Days	0	0	
Month to date heating degree days	0	0	
Since 1 June heating degree days	0	0	
Since 1 July heating degree days	0	0	
Cooling Degree Days	13	17	
Month to date cooling degree days	150	170	
Year to date cooling degree days	1581	1465	
Since 1 June cooling degree days	1085	1107	
Growing Degree Days	28 (Base 50)		

	Actual	Average	Record
Moisture			
Dew Point	75 °F		
Average Humidity	93		
Maximum Humidity	100		
Minimum Humidity	85		
Precipitation			
Precipitation	0.43 in	0.15 in	2.62 in (1966)
Month to date precipitation	3.81	1.56	
Year to date precipitation	50.98	34.60	
Sea Level Pressure			
Sea Level Pressure	30.09 in		
Wind			
Wind Speed	4 mph (SSW)		
Max Wind Speed	17 mph		
Max Gust Speed	21 mph		
Visibility	9 miles		
Events	Rain , Thunderstorm		

T = Trace of Precipitation, MM = Missing Value

Source: NWS Daily Summary

Daily Weather History Graph

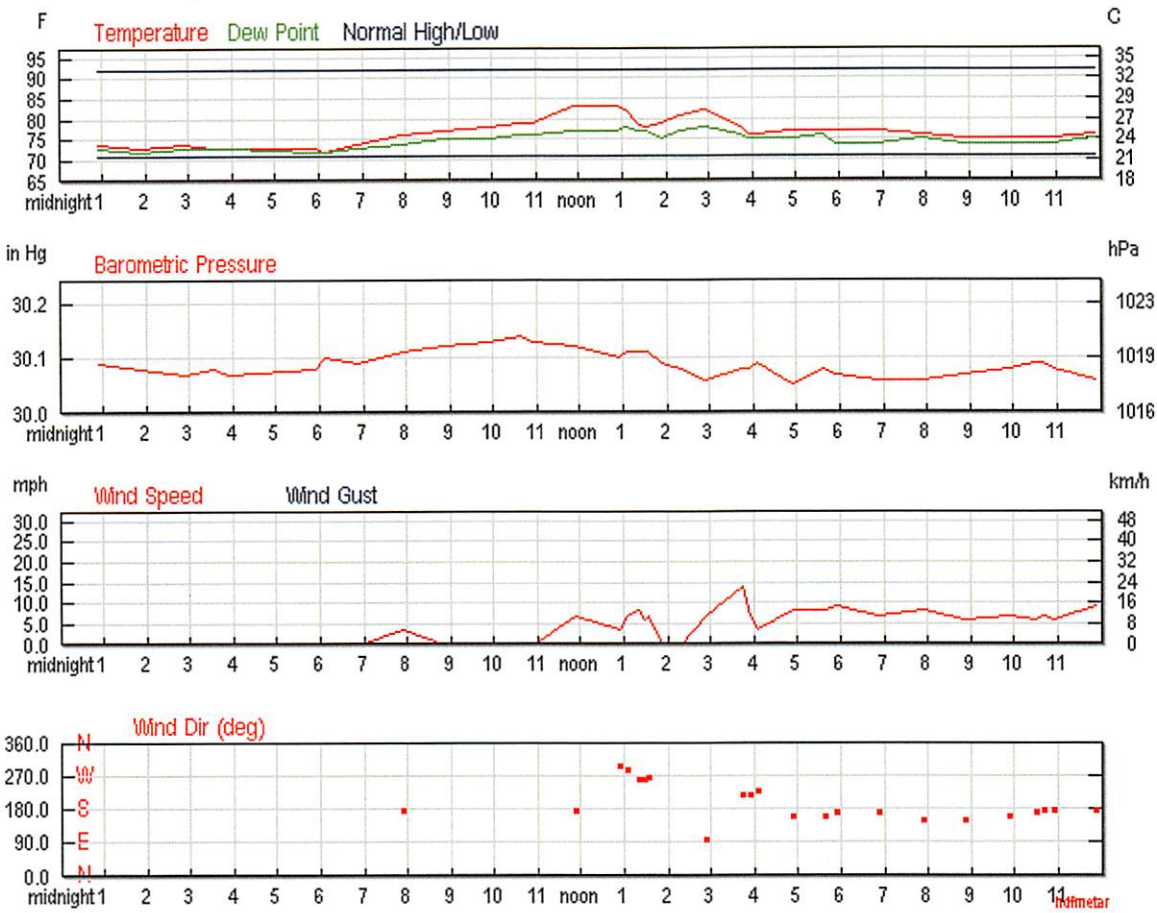

Search for Another Location

Airport or City:

Submit

Trip Planner

Search our weather history database for the weather conditions in past years. The results will help you decide how hot, cold, wet, or windy it might be!

Date:

Submit

Astronomy

Aug. 10, 2017

Rise

Set

Actual Time

6:21 AM CDT

7:49 PM CDT

**HISTORIC RENOVATIONS OF YAZOO
333 NORTH MAIN STREET
YAZOO CITY, MS 39194**

JOB REPORT: 08/11, 2017

MADISON COUNTY COURTHOUSE CUPOLA
CANTON, MS

WEATHER Hot - scattered rain

ACTIONS monitor access to roof by others

COMMENTS _____

Jackson, MS

Jackson-Evers International

© 9:38 AM CDT on August 16, 2017 (GMT -0500)

Weather History for KJAN - August, 2017

August

11

2017

View

Friday, August 11, 2017

Daily Weekly Monthly Custom


	Actual	Average	Record
Temperature			
Mean Temperature	84 °F	82 °F	
Max Temperature	93 °F	92 °F	103 °F (1954)
Min Temperature	74 °F	71 °F	59 °F (1990)
Degree Days			
Heating Degree Days	0	0	
Month to date heating degree days	0	0	
Since 1 June heating degree days	0	0	
Since 1 July heating degree days	0	0	

	Actual	Average	Record
Cooling Degree Days	19	17	
Month to date cooling degree days	169	187	
Year to date cooling degree days	1600	1482	
Since 1 June cooling degree days	1104	1124	
Growing Degree Days	33 (Base 50)		
Moisture			
Dew Point	75 °F		
Average Humidity	80		
Maximum Humidity	100		
Minimum Humidity	60		
Precipitation			
Precipitation	0.03 in	0.14 in	1.51 in (1984)
Month to date precipitation	3.84	1.70	
Year to date precipitation	51.01	34.74	
Sea Level Pressure			
Sea Level Pressure	30.03 in		
Wind			
Wind Speed	4 mph (SW)		
Max Wind Speed	9 mph		
Max Gust Speed	14 mph		
Visibility	8 miles		
Events	Rain , Thunderstorm		

T = Trace of Precipitation, MM = Missing Value

Source: NWS Daily Summary

Daily Weather History Graph

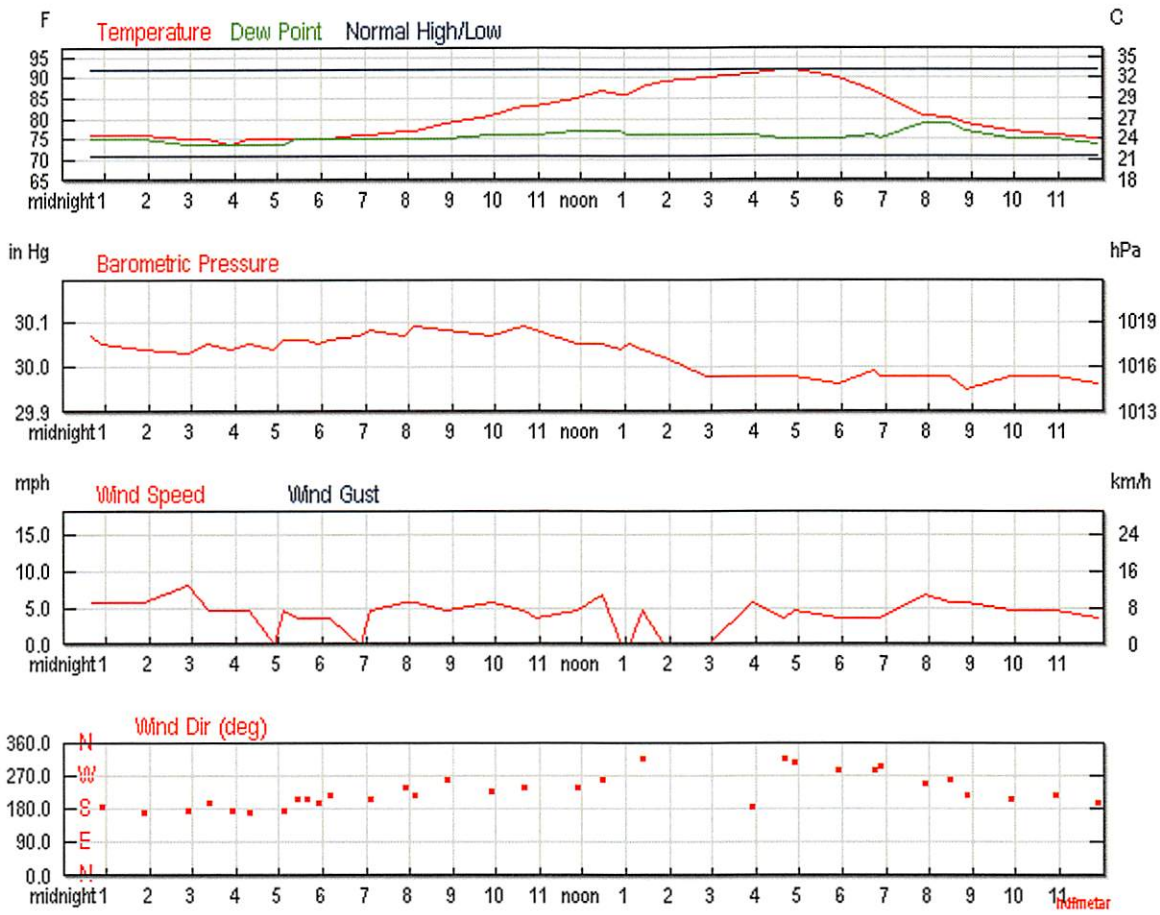

Search for Another Location

Airport or City:

Submit

Trip Planner

Search our weather history database for the weather conditions in past years. The results will help you decide how hot, cold, wet, or windy it might be!

Date:

Submit

Astronomy

Aug. 11, 2017

Rise

Set

Actual Time

6:21 AM CDT

7:48 PM CDT

**HISTORIC RENOVATIONS OF YAZOO
333 NORTH MAIN STREET
YAZOO CITY, MS 39194**

JOB REPORT: 08/14, 2017

MADISON COUNTY COURTHOUSE CUPOLA
CANTON, MS

WEATHER Hot - partly cloudy

ACTIONS paint prep crown + vertical tongue + groove

COMMENTS _____

Weather History for KJAN - August, 2017

August

14

2017

View

Monday, August 14, 2017

Daily Weekly Monthly Custom


	Actual	Average	Record
Temperature			
Mean Temperature	84 °F	82 °F	
Max Temperature	93 °F	92 °F	106 °F (2007)
Min Temperature	75 °F	71 °F	54 °F (2004)
Degree Days			
Heating Degree Days	0	0	
Month to date heating degree days	0	0	
Since 1 June heating degree days	0	0	
Since 1 July heating degree days	0	0	
Cooling Degree Days	19	17	
Month to date cooling degree days	224	238	
Year to date cooling degree days	1655	1533	
Since 1 June cooling degree days	1159	1175	
Growing Degree Days	33 (Base 50)		

	Actual	Average	Record
Moisture			
Dew Point	76 °F		
Average Humidity	76		
Maximum Humidity	100		
Minimum Humidity	52		
Precipitation			
Precipitation	0.00 in	0.15 in	1.19 in (2010)
Month to date precipitation	5.06	2.14	
Year to date precipitation	52.23	35.18	
Sea Level Pressure			
Sea Level Pressure	29.91 in		
Wind			
Wind Speed	6 mph (SW)		
Max Wind Speed	14 mph		
Max Gust Speed	18 mph		
Visibility	9 miles		
Events			

T = Trace of Precipitation, MM = Missing Value

Source: NWS Daily Summary

Daily Weather History Graph

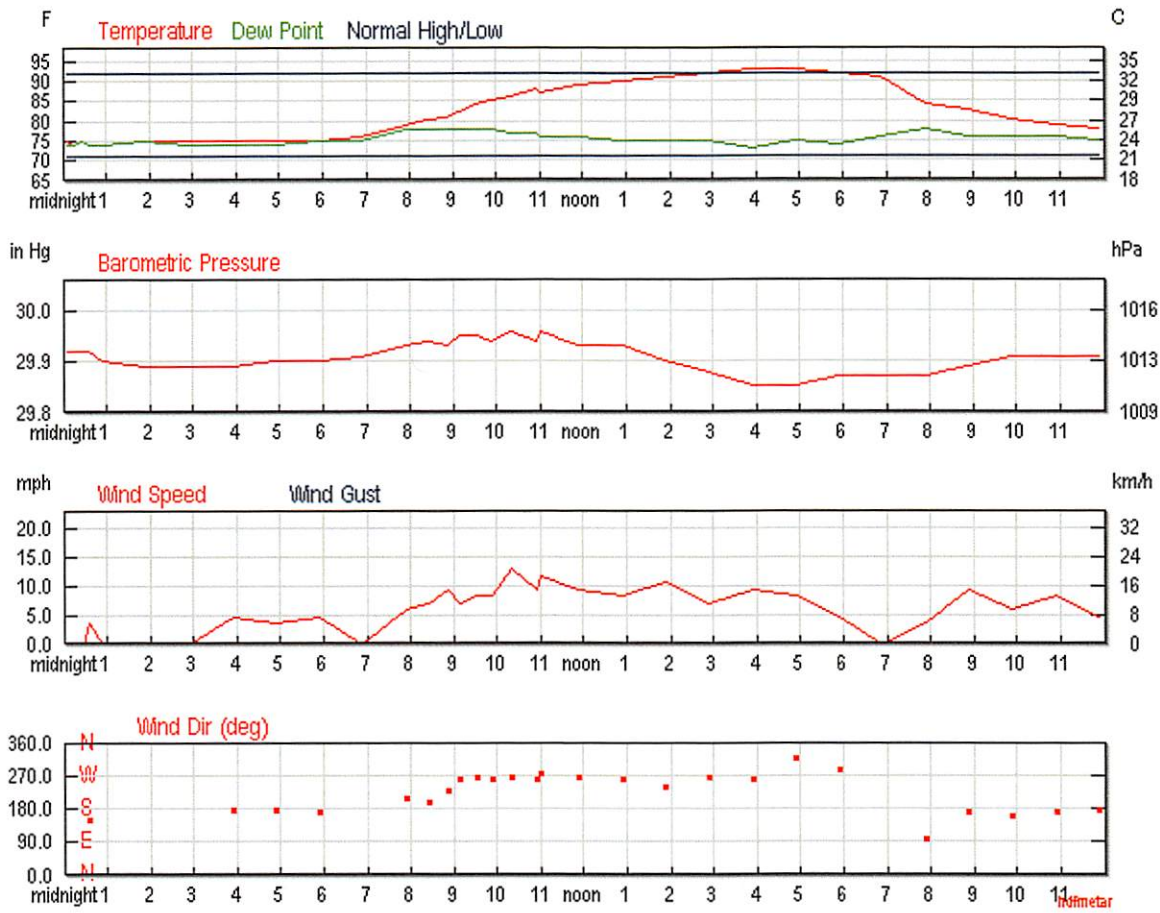

Search for Another Location

Airport or City:

Submit

Trip Planner

Search our weather history database for the weather conditions in past years. The results will help you decide how hot, cold, wet, or windy it might be!

Date:

Submit

Astronomy

Aug. 14, 2017	Rise	Set
Actual Time	6:23 AM CDT	7:45 PM CDT



**MADISON COUNTY COURTHOUSE
CUPOLA REPAIRS & RENOVATIONS
125 W NORTH STREET
CANTON, MS 39046**



**PARAMOUNT
CONSTRUCTION
GROUP, LLC**

234 West School Street, Suite B • Ridgeland, MS 39157 • 601-427-5454 office • 601-427-5456 fax

