

## **YANDELL ROAD WEST SEGMENT MADISON COUNTY BOARD OF SUPERVISORS 1<sup>ST</sup> QUARTER 2025 UPDATE**

Begin Contract Time: November 4, 2024

Contract Value: \$898,531.28

Amount Billed (3/31/25): \$185,742.34

Project Schedule: See Attached

Work Completed During Reporting Period:

- Topographic Mapping and Utility Survey
- Initial Resource Agency Consultation Completed
- T & E Consultation with USFWS Completed (Bat Surveys)
- Cultural Resource Survey complete and reports submitted to MDAH for concurrence

Work Planned for Next Reporting Period:

- Wetland Delineation and Submit to USACE for Concurrence
- Complete Noise Study
- Complete ROW Survey
- Conduct Geotechnical Investigations
- Continue Working on Field Review Plans (60% Plans)

Conceptual Design Approach:


Yandell Road will be widened to the south from the BOP to just past the western Deerfield entrance to a 5-lane section. The roadway will transition to a symmetrically widened 4-lane undivided section then back to a 5-lane section at the eastern Deerfield/Woodgate entrance and continue as a 5-lane section to the EOP just past Bainbridge.

# EXHIBIT C

## ESTIMATED PROJECT SCHEDULE

### YANDELL ROAD WEST SEGMENT

### NORTH OLD CANTON ROAD TO BAINBRIDGE CROSSING

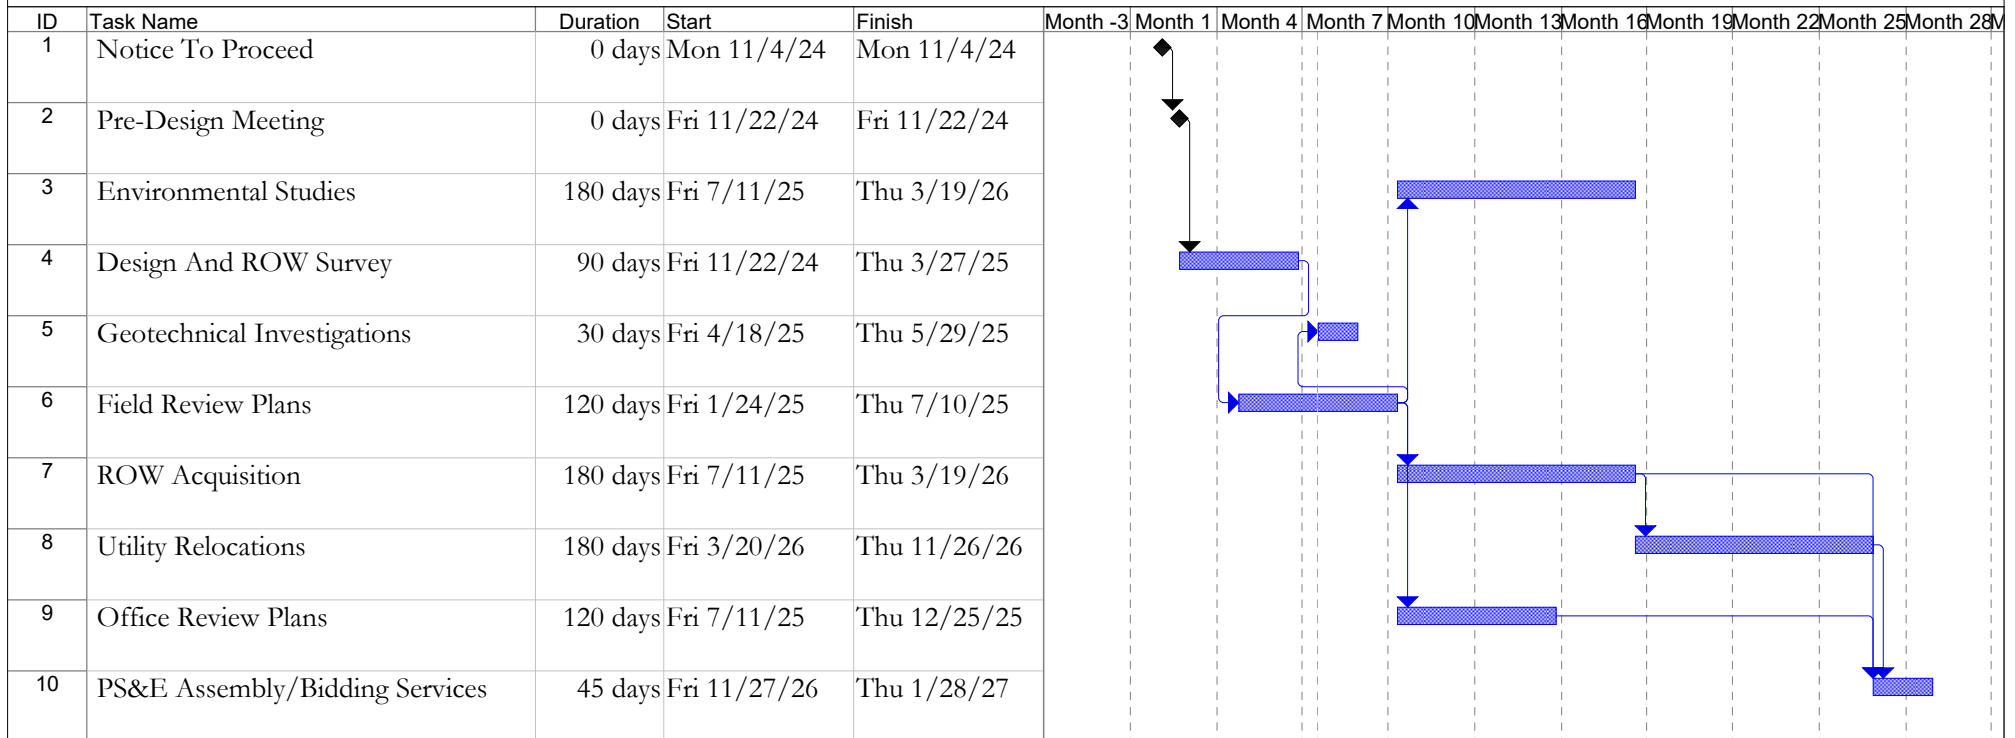

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Split	
External Tasks		Manual Summary			
External MileTask		Start-only			
